REBELLION BOUTIQUE

GROUP PROJECT REPORT – ASSIGNMENT 2

THE FIVE

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

Contents

Abstract 3

Introduction 4

Project Team (T.M 5 –) 5

Project Team Charter (T.M 5 –) 6

Literature Review (T.M 5 –) 8

Project Requirements (T.M 1 –) 10

Project Plan 12

- Gantt Chart (T.M 4 -) 12
- Project Risk Register (T.M 1 –) 14
- Personal Risk Register (T.M 1 –) 15
- Website Map (T.M 3 -) 16
- Work Breakdown (T.M 5 –) 17

Unified Modelling Language Diagrams 18

- Activity Diagram (T.M 3-) 18
- Sequence Diagram (T.M 1 –) 20
- PERT Chart (T.M 4 -) 21
- User Stories (T.M 5-) 22
- Critical Path Analysis (T.M 5 -) 23
- Use Case Diagram (T.M 4 –) 25

Project Components and Documentation 26

- Homepage Design (T.M 1 -) 26
- Mens and Womens wear Page (T.M 4 –) 27
- Adding Product to Shopping Cart (T.M 3 -) 28

Shopping Cart (T.M 3 -) 29
Checkout Page (T.M 1 -) 30
User Creating Account & Logging In (T.M 1 –) 31
Website Functionalities 33
Quick view product & Shopping basket panel (T.M 1 –) 33
Form to Contact Store/Staff (T.M 4 –) 34
Online Chat Facility (T.M 4 -) 35
Social Footer (T.M 4 -) 35
Products View of the Home Page (T.M 4 -) 36
Displaying Products (T.M 5 -) 38
Products Filtering (T.M 5 -) 39
Products Description (T.M 5 -) 40
Adding Products to Shopping Basket (T.M 5 -) 41
Editing Shopping Basket (T.M 5 -) 42
Testing Website 43
Signing Up (T.M 3 –) 43
Logging In (T.M 3 –) 44
Browsing of website (Links) (T.M 3 –) 45
Contacting Page (T.M 3 –) 46
Completing Payment (T.M 3 –) 48
Group Activities 49
Workload (T.M 1 –) 49
Deliverables (T.M 1 –) 50
Group Meetings (T.M 1 –) 50
Group Collaborations (T.M 1 –) 50
Group Meeting Minutes (T.M 1 –) 51
Challenges (T.M 1 –) 52
References (T.M 1, 3, 4 & 5) 54

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

Abstract

This project aims to build an e-commerce website that sells high value clothing, specifically, a website that meets users' requirements and expectations. To meet users' requirements, we developed user stories and all team members were required to investigate and study the functionalities of their favourite online clothing stores. The project was only for academic purpose. The project was done by a team of five members who has different skills.

The project was divided into four phases, consisting of planning, components and documentation, design, and testing. Members were assigned tasks based on their skills. We used the critical path analysis method to estimate time and create Gantt chart. Pert chart was used to map out schedules and tasks with the project. Weekly meetings were conducted to plan sprints during each phase. Risk assessment was carried out and mitigation actions were written down to ensure that the project was completed in time. The design of the website was done on the WIX platform.

At the end, we were able to create a functional website that customers can search for items, select items, place items in the basket and proceed to checkout. Team members gave in their full efforts; however, the website is not full proof. There is always room for improvement.

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

Introduction

For this project report we have been asked to demonstrate our group work towards completing our aim in building a website – to successfully do this as a team we will ensure to provide information of a literature review which will show the investigations we have done in project management as well as software methodologies.

Besides this, the report will include evidence of our project planning, within this area of the report Gantt Chart, Work Breakdown Structure, Product Backlog, Risk Analysis along with Critical Path analysis will be shown.

Our team will also be working in demonstrating the techniques that will be used for our project such as case diagrams, we'll also get one of team members to test the website which we created whilst other two team members will be focused on documentation and labelling screenshots of our website. Lastly, our team leader will ensure to provide evidence of teamwork for example, allocation of team roles, collaboration, group meetings.

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

Project Team (T.M 5 –)

Team Member 1 - Project Leader & Presentation

- Leads project team meetings
- Documents meeting minutes
- Provides report on task progresses
- Oversee work schedule
- Prepare a structural design report
- PowerPoint presentation

Team Member 2 - Web designer, UX Designer and Web developer

- Creates design plans and website structure
- Designs the visual images for the website
- Website mapping
- Builds the website on WIX platform
- Explains design ideas and website functionalities
- Content control

Team Member 3 - Database Developer

- Designs database systems
- Test databases
- Provides an operational manual for users
- Uses ER diagrams to show the logical structure of the database.

Team Member 4 - UML Designer

- Gantt chart
- Pert chart
- Use case diagram
- Critical Path Analysis
- Sequence diagram

Team Member - 5 Quality Assurance and Documentation

- Test the web-based publication: client-side scripting, hyperlinks, browser compatibility etc.

- Test the web-based content: viruses, spelling, grammar, punctuation, media etc.
- Test Accessibility: page featuring, markup usage, style sheets etc.
- Conduct user survey and report feedback
- Conduct literature review
- Creates project methodology

Project Team Charter (T.M 5 –)

Team Name	The Five (Group 14)
Project Name	Rebellion Boutique
Duration	8 weeks
Team Members and Roles	• xxxxxxx [Project Leader] • xxxxxxx [Web Developer] • xxxxxxx [Quality Assurance] • xxxxxxx [UML Designer] • xxxxxxx [Database Developer]
Purpose	The purpose of this team is to develop an e-Commerce website that sells designer clothes.
Goals	Our goals are: • To understand user needs. • To create a website that engages our visitors with user friendly interfaces and offer quality designer clothes that will ensure customer satisfaction. • To provide a website that administrators (staff, executives, contractors) can interact with easily and to increase sales.
	• Submit individually assigned tasks on time.

Objectives	• Meet deadline of the project • Present a functional website. • Acquire new knowledge and experiences by the end of the project. • Get the highest possible marks. • Build our personal growths as we learn from each other
Values	• Customer focus • Tasks completed on time • Committed to achieving project goals. • Cooperation among team members • Mutual respect among members • All members are equal • Support each other
Strength and Assets	• Diversity • Hands on abilities • Experience in online shopping • Fast learners • Good communicators
Weaknesses	As members of the team has their own personal commitments, this can make it difficult to schedule meetings. It can also affect deadlines.
Expectations	• All members are expected to be involved in the project. • We expect to meet the project deadline. • We expect all members to complete their assigned task. • We expect that all misunderstandings will be resolved quickly through communication.
Milestones	• Create all UML diagrams by 01/04/22 • Website design by 06/05/22 • Testing by 11/05/22 • Documentation and reports by 17/05/22 • Review by 19/05/22 • Submission 20/05/22
Resources	• WIX platform for building website. • UWL blackboard for communication and sharing of files. • Microsoft word for documentations

	• Teams for meetings

Literature Review (T.M 5 –)

This page discusses and reviews the relevant and existing literature on project management and different methodologies with a focus on the Agile Scrum methodology. It will include the reason why we have chosen agile scrum and how scrum was implemented during the project cycle. The professional organization, Project Management Institute defines project management as the use of specific knowledge, skills, tools, and techniques to deliver something of value to people. (Project Management Institute, 2013)A project management methodology is basically the principles and practices that help to manage a project to achieve optimum performance.

Main Body

History of project management methodologies

According to Seymour and Hussein (2014), humans have successfully completed projects long before the initiation of the term project management. They explained that ingenious architects and engineers have delivered impressive projects such as The Great Wall of China, the Pyramid of Giza, and the Stonehenge without the use of any software but rather by carefully thinking about all the processes of the project, starting with the initiation and planning phases to the execution and monitoring all the way to the closing. These projects can be argued to be among the best examples of project management. In 1917, Henry Gantt created a scheduling diagram called the Gantt chart which was used in the Hoover Dam project in 1931. In 1957, the Dupont Corporation invented the Critical Path Method used to estimate project duration and to address the complex method of shutting down and restarting a chemical plant. In 1958, the U.S Navy formulated and documented the modern principles of project management methodologies and techniques known as PERT. PERT is used to analyse the tasks involved in completing a project by breaking the project into smaller tasks with the assigned minimum time needed to complete each task. In 1962, the United State Department of Defence developed the Work Breakdown Structure that was used in its projects. In 1977, Oracle and Artemis created project management software due to technological advancement. In 1989, the UK Government's Central Computing and Telecommunications Agency published the Projects in Controlled Environments (PRINCE) as the UK standard for all government information projects.

Modern project management methodologies

Over the years, different project management methodologies have been developed for different projects. The two major methodologies are Traditional (Waterfall) and Agile project management. With the traditional methodologies, the goal is to carry out tasks in a predetermined orderly sequence: requirements, analysis, design, construction, testing, deployment, and maintenance. Though the waterfall methodology is simpler, it has some disadvantages which led to hindering workflows.
Teams were required to stick to the pre-determined requirements unable to make changes. The project manager is responsible and accountable for the project results.
This rigidness of the Waterfall led to the development of the Agile Manifesto by the 17 software developers in 2001 which became the guiding principle of the Agile Project Management models. The agile methodology gives users the flexibility that Waterfalls doesn't give. Agile methodologies are collaborative, quick and open to change.

Why we chose Agile Methodology (SCRUM)

Since agile was originally created within the context of software development we agreed it will be effective in the arena of website development. Although there are many different project management methodologies that are used to implement the Agile philosophy, we decided to use the Scrum methodology after considering our team size, risks, and timeline. Our goal was to create a website for high-end clothing retail and as such needed the involvement of all team members. Scrum helps to complete project deliverables more quickly and efficiently. Scrum is said to be suited for projects that are likely to experience change, just like websites.

How we used SCRUM

Using Scrum allowed us to identify the work, identify who will do the work, how it will be done and when it will be completed. The team was able to collaborate and meet weekly to conduct a sprint planning session where tasks necessary to meet product backlog were broken into small manageable tasks. We decided on a time duration for each spring. We used Microsoft teams, UWL blackboard as well as WhatsApp group chat to communicate with a scrum leader available to guide the team and keep the team in focus.

Conclusion

Like every methodology, we realised that Scrum also had a few disadvantages. Some of the disadvantages we faced with using Scrum was that the weekly meetings sometimes frustrated team members. We realised that the chances of the project failing was high if a team member is not cooperative or committed.
We were able to overcome these disadvantages with proper planning and well-defined goals and responsibilities plus helping each member to accomplish their assigned tasks.

Project Requirements (T.M 1 –)

Within the project that each member has been working on, there are several project requirements which must be fulfilled to ensure the success of this group project – as we are designing to implement an E-Commerce Website for the retail company Rebellion Boutique. Several things were taken in consideration for example, who was going to use the website, whether it was easy to use, if it included images for the user to have an idea of how the product would look like etc. As a team we focused on the previous requirements that were listed in the presentation and expanded on these requirements by concentrating on each page, as the main objective is to ensure many users can complete a purchase through the website "Rebellion Boutique" without any complications.

Home Page:

- Include a company logo
- Drop down menu of categories e.g., womenswear, menswear
- Logging In Link
- Cart Link
- Search Bar
- Pop-Up "Let's Chat" button
- Social Footer links e.g., Instagram, Facebook & sign up to Newsletter box
- Customer Service contact information
- Exhibiting most popular products inc. price & product name

Shopping Basket:

- Quantity adjustment for products
- An "X" to remove items
- Adding items
- Entering discount codes
- Checkout Page Link
- Details of items e.g., product name & price, size chosen
- Images of all products in shopping basket

Checkout Page:

- Customer's name and email
- Customer's address
- Shipping details e.g., name, mobile number
- Shipping Address
- Payment Details
- View their Order Summary along with product image
- Edit shopping basket
- Complete Purchase button

Logging in and Creating Account Page:

- Logging in details – email address and password
- Sign In button
- Create an Account button
- Customers email address and new password
- Customers details name, last name, and title

Browsing Products by Category:

- Filter products by price, brand, size, colour etc.
- Attractive product images
- Product name and price labelled

Adding product to shopping cart:

- Product image from various angles
- Product description
- Product name and price
- Size Selection
- Quantity of item needed
- Add to basket button
- Social Media Links

Admin Page:

- Website editing tools
- Manage the stock
- Analytics Overviews
- Adjusting orders

Project Plan

GANTT CHART (T.M 4 -)

For the success of the project, Gantt chart have been a vital tool in ensuring the team meets all the objectives and goals set out. The Gant chart is such a powerful tool in supporting the creation of the website, from providing us with time scale to dependencies of objectives and functionalities of the whole process.

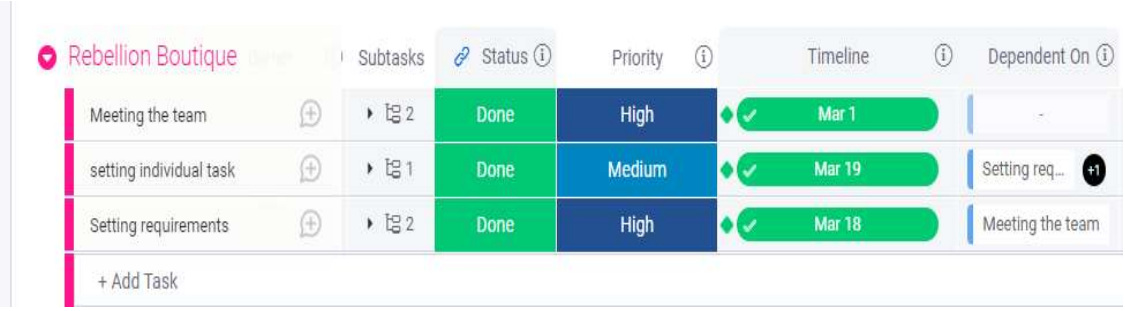

Rebellion Boutique	Subtasks	Status	Priority	Timeline	Dependent On
Meeting the team	2	Done	High	Mar 1	-
setting individual task	1	Done	Medium	Mar 19	Setting req... +1
Setting requirements	2	Done	High	Mar 18	Meeting the team
+ Add Task					

The image above is a clear illustration of what the Gant chart offered, starting from status, priority, timescale, and dependencies.

The status is so important as it requires us to update the chart once a requirement is completed and the ones that are yet to be completed or work under process are left with an orange mark. Which serves as a reminder to the whole group, and probably a bit of pressure to help push the team to get work done.

Live		Working on it	High	May 18 - 20
+ Add Task				

The orange marker set the difference between an objective that is completed (green marker) to the ones that are not.

Timescale

Another important functionality from the use of the Gant chart is the timescale. The timescale is so powerful as it helps to avoid missing deadlines and helps the team to manage their work. While creating the website

requires several objectives and requirements to be completed before finishing the whole website creation, there are stages that needs to be completed before jumping into another. And to meet up with deadlines, the team needs to adhere to the timescale given for every aspect of the requirements. So, the timeline serves as a reminder for the whole team.

Deployment	Subtasks	Status	Priority	Timeline	Dependent On
Unit Testing	2	Done	High	May 4 - 13	Creating interfa...
Regression testing	1	Done	High	May 13 - 16	Unit Testing

We can clearly see the difference between each objective here e.g., Unit testing will be conducted from the from the 4th of May to the 13th, whilst regression testing follows up if any correction was made from the unit testing to check if any changes made is corrected and does not affect other functionalities of the website.

Dependencies

Dependencies is probably the most or if not the most important features of using a Gantt chart as it helps with a lot of things e.g., helps the team to manage work better i.e., its helps in planning whilst creating the website like making sure one thing gets done before the other. Below are examples of how using the Gantt chart helped with division of requirements and planning process

Building the website	Subtasks	Status	Priority	Timeline	Dependent On
Creating interfaces	1	Done	High	Apr 22	Setting require..
Logos and Name		Done	High	Apr 22	setting individu..
Menu Bar	5	Done	High	Apr 23	Creating interfa...
User	3	Done	High	Apr 23	Creating interfa...
Product description	6	Done	High	Apr 22	Menu Bar
Unit Testing	2	Done	High	May 4 - 13	Creating interfa...
Regression testing	1	Done	High	May 13 - 16	Unit Testing
Requirements Test	1	Done	High	May 6 - 13	Setting req... +1

The illustra which are building th g to occur, there are thi ements that are agreed to website to have been cr

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

PROJECT RISK REGISTER (T.M 1 –)

It's significant to be aware of potential risks, which why as we have created a risk register to demonstrate some of the identified risks – we'll use this table below weekly to stay aware of the risks to prevent it as it can impact the process of the project negatively.

ID	RISK DESCRIPTION	SEVERITY	OWNER	MITIGATING ACTIONS	CONTINGENT ACTIONS	PROGRESS BASED ON ACTIONS	STATUS
1	Development Costs are inaccurate	HIGH	PROJECT DEVELOPER	Meet with client and finance team to seek why costs aren't accurate	Recalculate all costs in a timely manner to find where the mistake is and meet with team and client to discuss the issues	Verifying costs weekly to avoid confusions	OPEN
2	Schedule not met	MEDIUM	PROJECT TEAM	Inform client of delays and meet with team	Conduct meeting with all team members and verify who's able to take up on extra work	Reschedule date of completion confirm with client and team	OPEN
3	Unplanned work must be accommodated	HIGH	PROJECT LEADER	Must be present in project meeting – check all tasks and understand all plans	Set dates and times for each member to complete a task – meet to discuss new tasks which have been added	Project leader and project manager should conduct these meetings to avoid falling back in time.	OPEN
4	Lack of Communication – confusions and no clarity	MEDIUM	PROJECT MANAGER	Scheduling a group meeting to ensure each member understands all tasks given.	Meeting on weekly basis and planning of what the next tasks will be ahead of time.	Meetings have been scheduled and agreed by everyone	OPEN
5	Extreme Weather	HIGH	PROJECT TEAM	Back-Up emergency project, insurance in place.	Due to safety, meetings would take place via online or scheduled a different date.	Alternative meeting date if extreme weather occurs	OPEN
6	Various scope changes	MEDIUM	QUALITY ASSURANCE	Prioritize features – have a sketch of Scope before submitting a final scope	Meet with team members and get some feedback, share plans to avoid making many changes	Review scope weekly and meet with team before finalising scope	OPEN
7	Insufficient funds for project	LOW	PROJECT LEADER	Ensure all finances and fees have been calculated carefully	Reduce costs by removing expensive features or set a meeting with client increase funds	Working within the budget given by client and regularly check funds	OPEN

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

PERSONAL RISK REGISTER (T.M 1 –)

When completing a project, a personal risk register is required for all team members, so for this section of the report, I have shown a table of my personal risks, I will review this table weekly to help me complete all my assigned tasks in time and avoid any issues.

ID	RISK DESCRIPTION	SEVERITY	OWNER	MITIGATING ACTIONS	CONTINGENT ACTIONS	PROGRESS BASED ON ACTIONS	STATUS
1	Time Management	HIGH	Project Leader	Must be present in project meetings and arrive 15 minutes before. Plan the journey.	Set up a plan journey with team member to ensure everyone is on time.	Project leader should ensure meetings have been set-up as well as checked travel updates	OPEN
2	Not enough knowledge of Sequence Diagrams	MEDIUM	Project Leader	Must communicate with UML team to get a better understanding, research	Set up a date to research about a given topic to increase knowledge	Project Leader and UML team to discuss any doubts	OPEN
3	Personal problems	LOW	Personal, Project Leader	Must prioritise the project to avoid failing and handle personal problems outside of work	Keep up with the assigned work and avoid sharing personal problems with team as it could slow everyone down	Project Leader completing assigned tasks efficiently	OPEN
4	Cancelling meetings	MEDIUM	Personal, Project Leader	Scheduling a group meeting to ensure each member understands all tasks given.	Meeting on weekly basis and planning of what the next tasks will be ahead of time.	Meetings have been scheduled and agreed by everyone	OPEN
5	Lack of communication with team members	HIGH	Project Leader and whole team	Must communicate with team individually and together	Catching up with everyone to verify if anyone needs support	Team must meet up and share any doubts or opinions	OPEN

As shown above, I have listed two high risks which are Time Management and Lack of Communication with Team Members, I must work on these risks as it could affect the project negatively due to my lack of time management – I must ensure to keep up communication with all team members so we can always be organised and avoid lacking.

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

WEBSITE MAP (T.M 3 -)

The website map or site map is the blueprint of the website that illustrates how the website pages are connected to each other, it is the structure behind the website that helps the search engines to find the website. The search engines will be using the site map to find different pages of the website.

Below is a diagram of showing how the website map is created and how related pages are connected.

Home Page: This is the main page of the website that will be shown to the user upon browsing the site: Home, Collection, Customer Care, Login, Search Bar, Team, Address, Cart.

Collection: Women, Men, Accessories, Sale.

Customer Care: Does not contain any subpages, this page is for communication where customers can inquire and send message to the seller.

Visit Us: Does not contain subpages, provides information about the seller and working hours as well as the address.

Team: Provides information about the team.

Cart: contains all the added items and purchase page.

Login: this page contains a subpage where account can be created or sign.

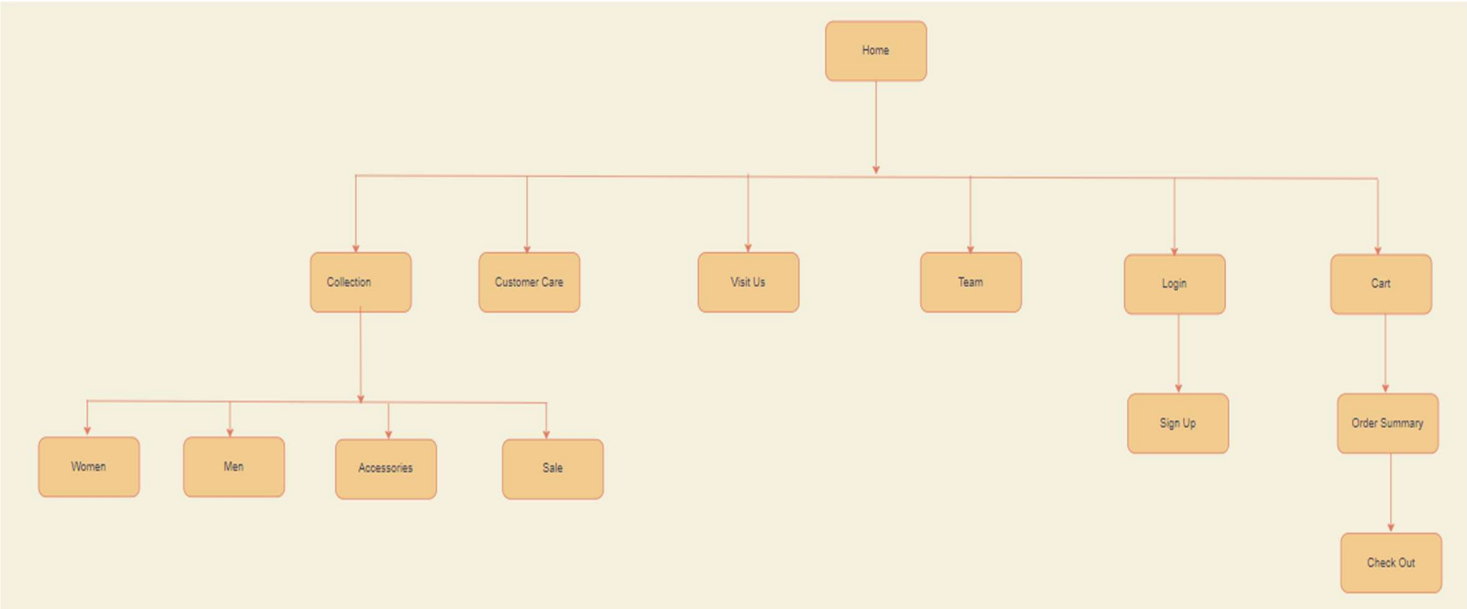

WORK BREAKDOWN (T.M 5 –)

"Concurrently with the time-based plan a work breakdown structure (WBS) should also be produced and included in the project management plan, which will provide all those involved in the project with a hierarchically structured division of the work required in the project. Keith and Gordon (2006, p. 24). WBS allowed us to break the project into smaller phase and deliverable based components. This made the project less overwhelming and more manageable.

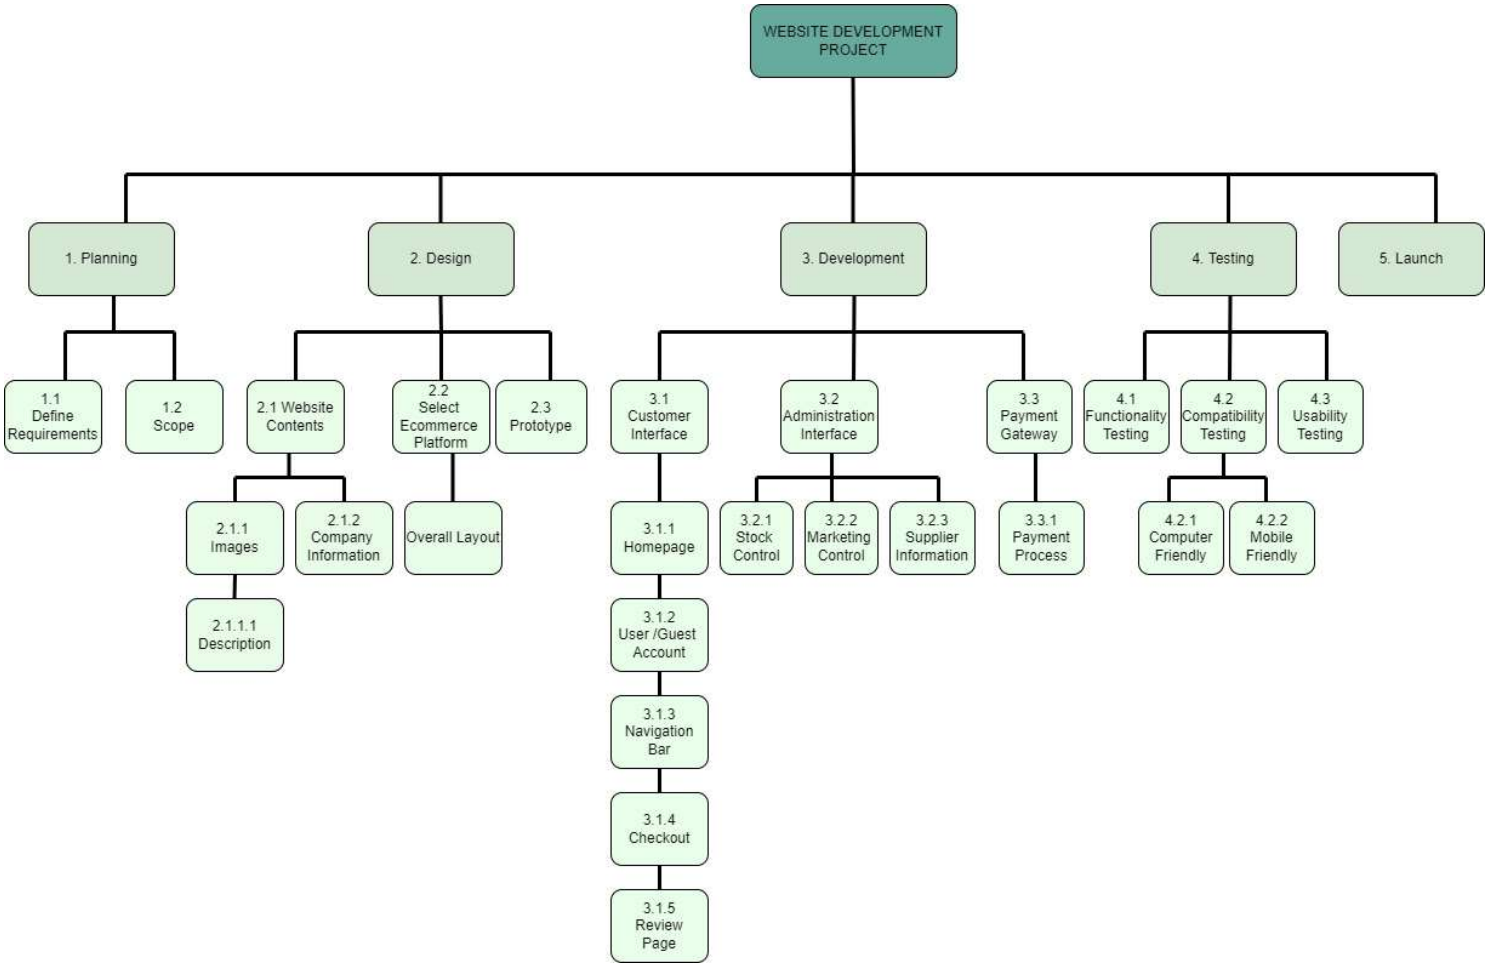

The above diagram provided a roadmap for the team working on the project allowing members to focus on their specific tasks.

Unified Modelling Language Diagrams

The unified modelling language aims at providing visual explanations and details in relation to how the website is designed and what it does.

The UML offers a standard method of writing systems blueprints and how the system functions.

ACTIVITY DIAGRAM (T.M 3-)

The purpose of activity diagram is to capture the behaviour of the system, it visually presents a series of actions of flow of control in a system.

The diagram illustrates the possible actions that be performed by a user or an administrator.

USER:

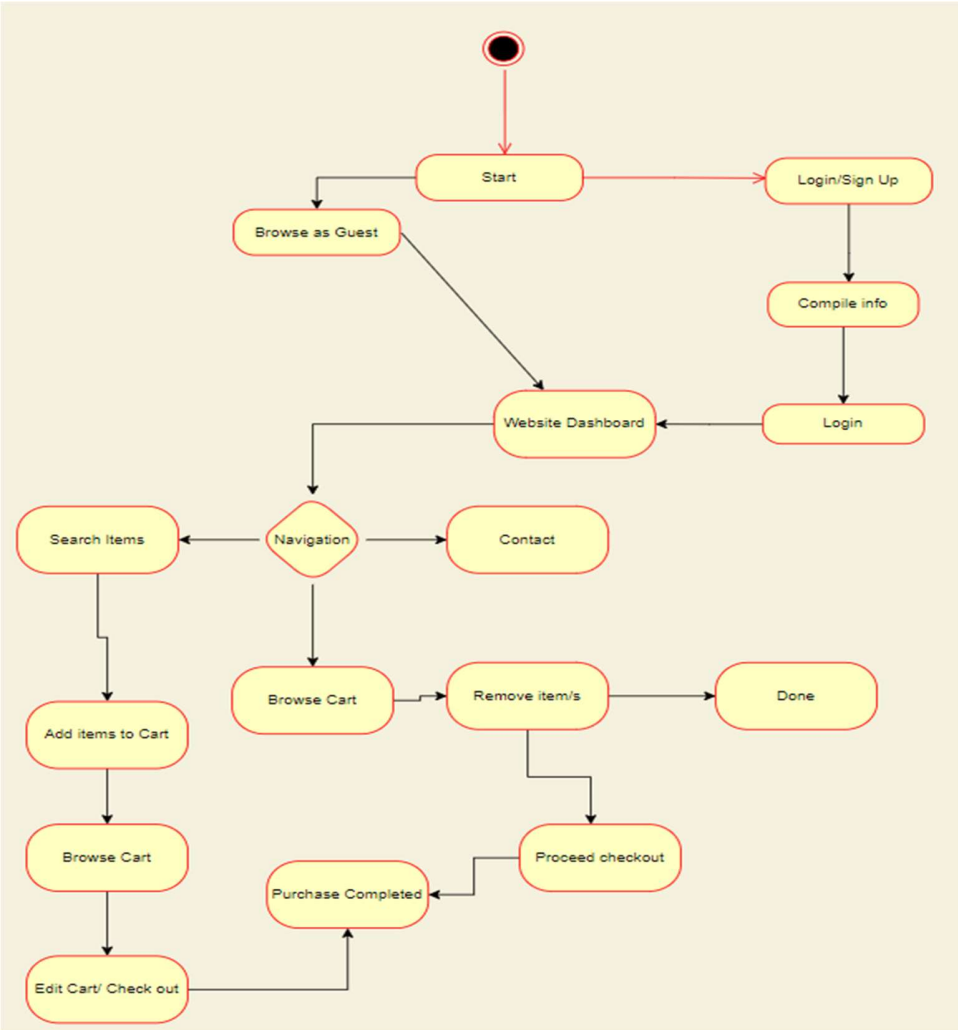

ADMIN:

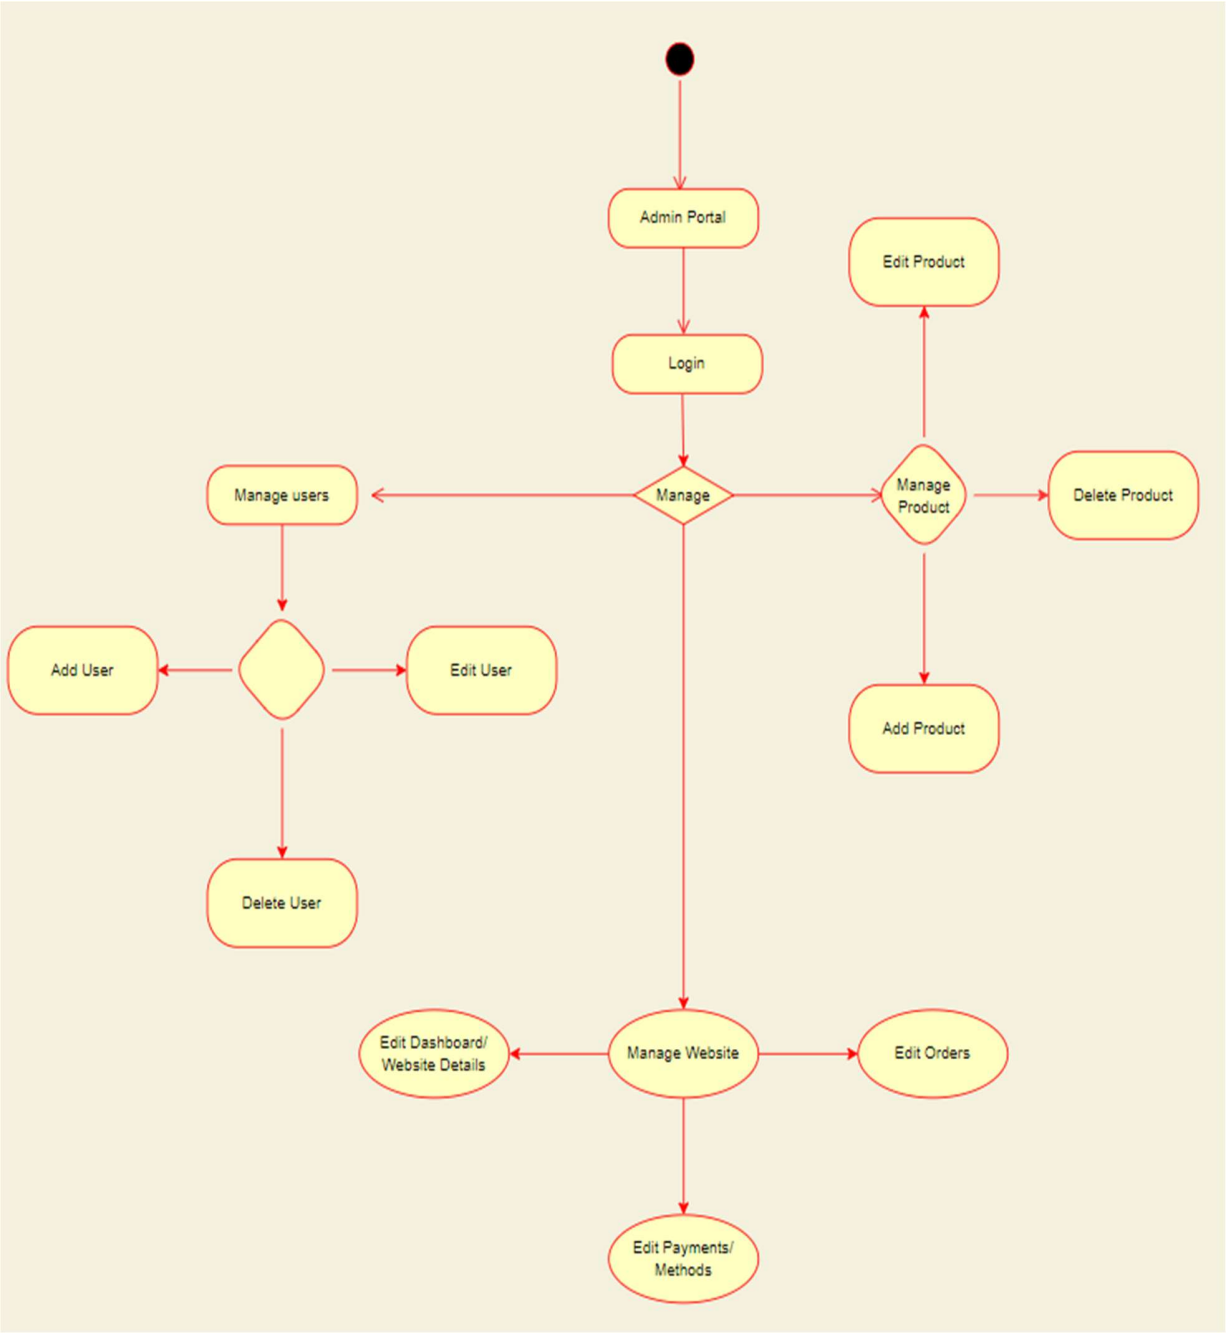
Admin Portal
Login
Manage
Manage users
Manage Product
Edit Product
Delete Product
Add Product
Add User
Edit User
Delete User
Manage Website
Edit Dashboard/ Website Details
Edit Orders
Edit Payments/ Methods

SEQUENCE DIAGRAM (T.M 1 –)

Below there's a sequence diagram which has been created – this type of diagram is part of Unified Modeling Language also known as UML, this sequence diagram simply demonstrates the interaction which will occur between the admin towards the website and server as well as the interaction the client will have with the developed website. For example, the user may want to log into their account, for this to be successful it will communicate with "Access Account" and will verify their password before any approval. In the diagram below it clearly shows several arrows pointing from User towards Website – this simply shows how the user will be requesting specific things such as browsing the available products, being able to select the products, adding items to shopping cart etc.

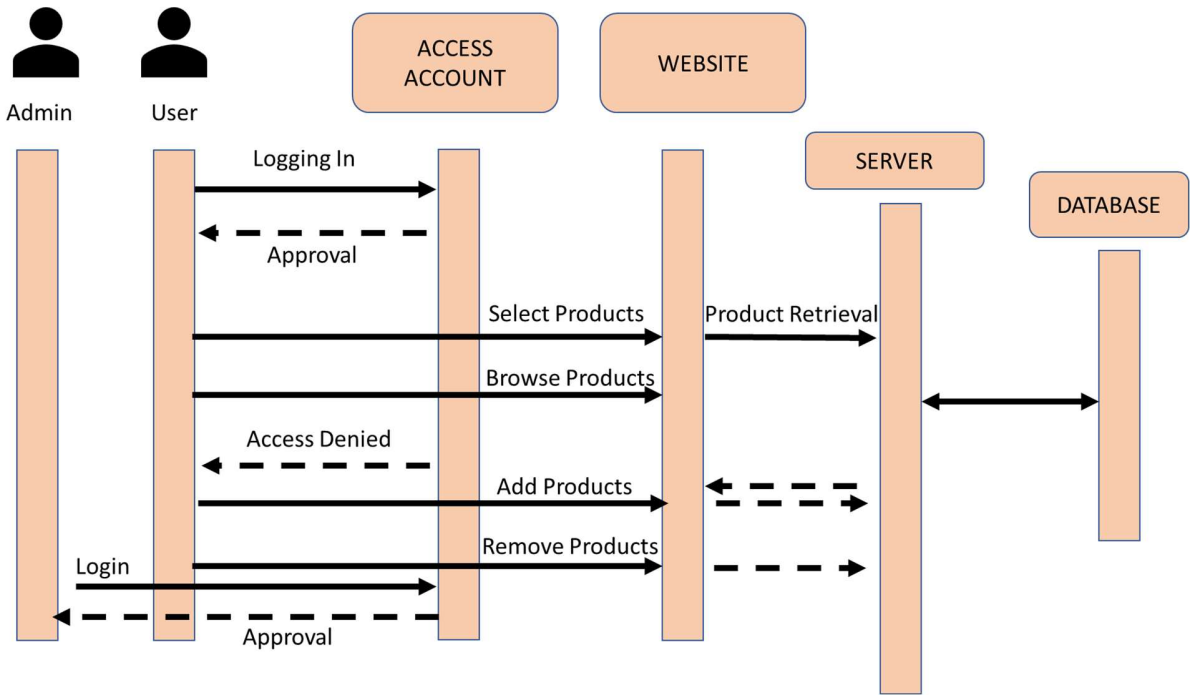

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

PERT CHART (T.M 4 -)

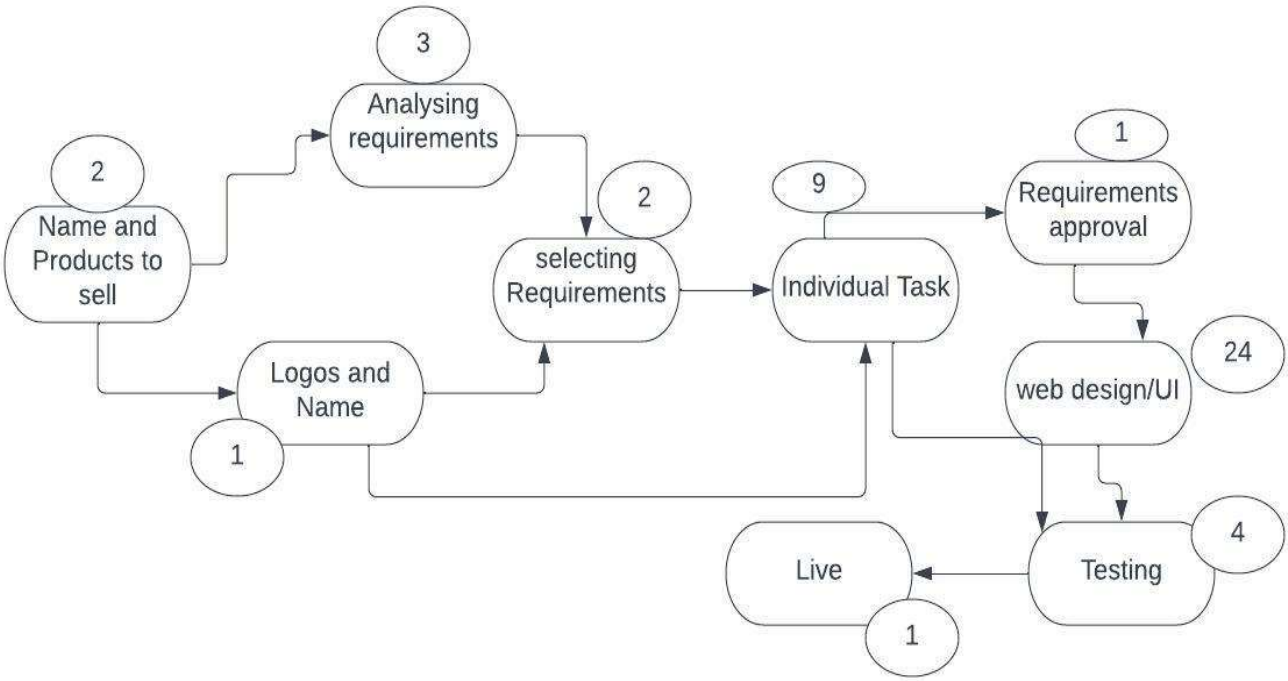

The pert chart above is also one of the most important charts used in estimating and measuring the time it takes for each objective/requirement to be achieved. Also, from the diagram, we can see arrows linking one objective to the other. This means dependencies and this helped with the whole planning process in deciding what to do next.

USER STORIES (T.M 5-)

Although the assignment clearly stated what is expected to be included on the website, we needed to understand how to link the various components and functions to provide good value product to the users. We identified our users and created below few user stories.

Search Button

- As an online customer

I need to search for products

So, I can find the ones I want to buy.

User Account

- As a customer

I need to authenticate myself

So that I can see my details, saved items and past orders.

Card Authorization

- As a customer about to purchase a product

I need to submit my card details and get authorization

So, I can complete my checkout.

Register

- As an Admin

I need to register on the website

So that I can log on the website.

Logging in the system

- As an Admin

I need to log into the system

So, I can control product stock.

CRITICAL PATH ANALYSIS (T.M 5 -)

Critical Path Analysis shows a list of detailed tasks based on the Work Breakdown Structure. It shows the dependencies of tasks and the time of completion. The Critical Path Method was used to calculate the project's duration from start to finish and to identify the critical path of the project. It calculates the early and late start as well as the early and late finish.

TASK ID	TASK	PREDECESSOR	TYPE	DURATION (IN DAYS)	EARLY START	LATE START	EARLY FINISH	LATE FINISH
A	Project Initiation		Sequential	0	0	0	0	0
B	Planning	A	Sequential	4	0	0	4	4
C	Defining Requirements	B	Parallel	5	4	4	9	9
D	WBS, Gantt Chart	C	Sequential	2	9	11	11	13
E	UML Diagrams	D	Sequential	5	11	13	16	18
F	Gathering data for the Database	C	Sequential	3	9	9	12	12
G	Database Prototype	F	Parallel	4	12	12	16	16
H	Database Creation	G	Sequential	6	16	16	22	22
I	Website Prototype	E	Sequential	4	16	18	20	22
J	Website Creation (page layout, navigation, etc)	H, I	Sequential	20	22	22	42	42
K	Content Writing and Assembly	J	Parallel	6	42	42	48	48
L	Testing and reviewing	K	Parallel	10	48	48	58	58
M	Launch	L	Sequential	1	58	58	59	59
N	Report Writing	A, M	Parallel	10	59	59	69	69
O	Finish			1	69	69	70	70

From the chart, every task that must be done to get the project completed has been listed. Predecessors show the correct order of tasks. Following the order should be the priority. Tasks that are labelled as sequential are tasks that can only begin after another task has ended. Parallel tasks are tasks that can begin alongside another task.

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

NETWORK DIAGRAM

Earliest Start	Task	Earliest Finish
Latest Start	Duration	Latest Finish

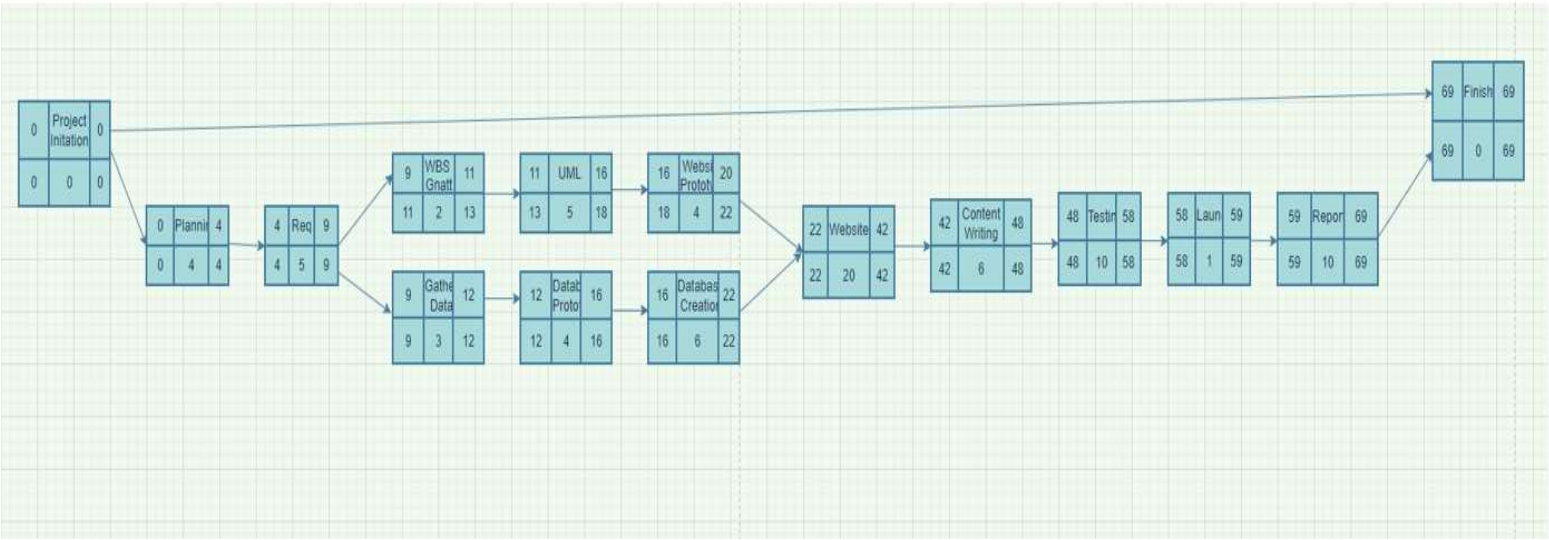

The ideal critical path would be project initiation -> planning -> defining requirements -> gathering information -> database prototype -> database creation -> website creation -> content writing -> testing -> report writing -> finish. It means that, if there is any delay in any of the tasks in the critical path, it will affect the entire duration of the project.

USE CASE DIAGRAM (T.M 4 –)

The use case diagram below shows every kind of interactions that could exist for every individual user within the company i.e., from the customers to the staff. Customers use the website to access our products and services with the aim of buying. One of objectives is attracting more customers to the brand, and the website environment has been made accessible for both new and existing customers interaction. Furthermore, we have the staff as well who ensures all activities on the website are smooth from replies to active interaction with the website to enable good user experience for our customers.

The diagram is represented with arrows explaining the connections with different users (customers and staff). On the left side of the diagram is the activities and interactions that could occur with the use of the website. Hence, on the right, we have every reaction that could occur from using the left activities. And they are split into two. One called include and the other is called extend i.e., for every activity, there must be a reaction: which is what include is doing. Whilst extend is the aftermath of the reaction i.e., if an activity is failing, there's always provision for an alternative support.

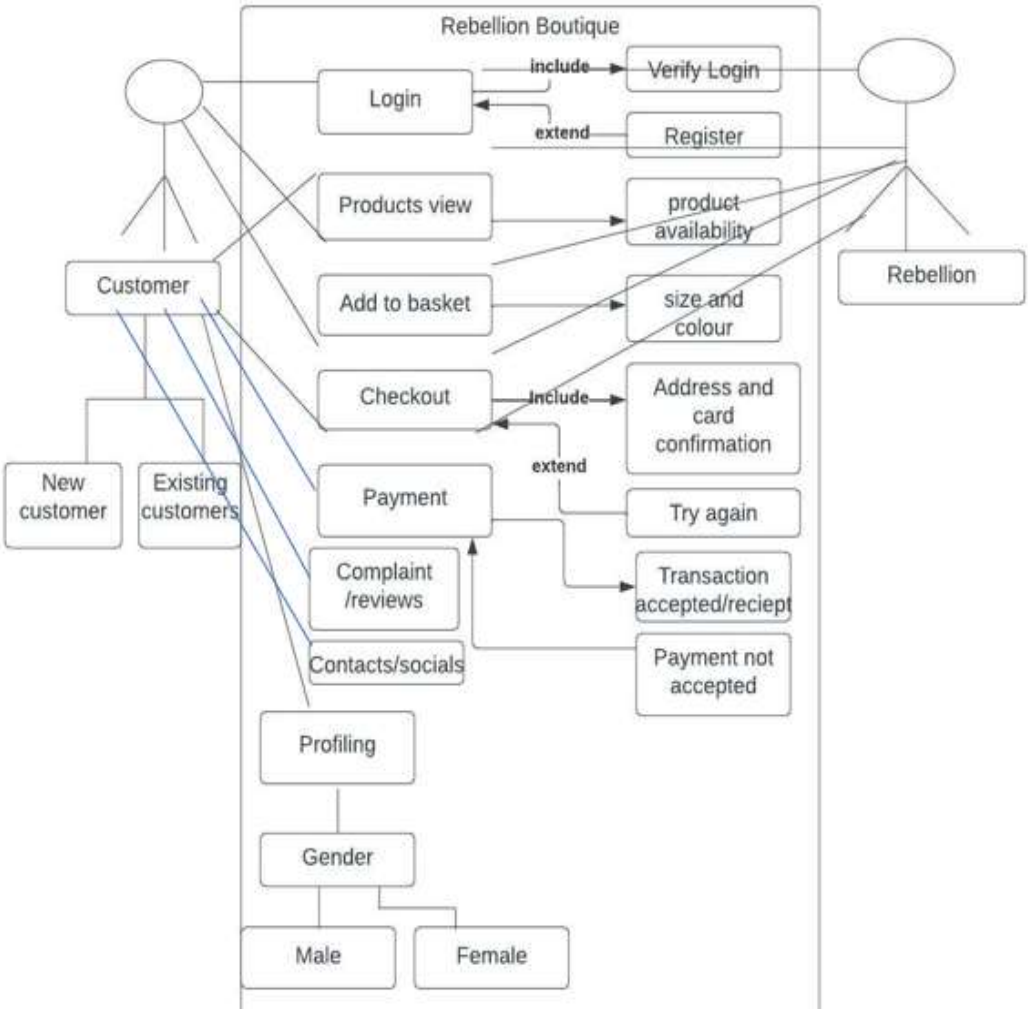

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

Project Components and Documentation

Justification and Explanation of Design:

HOMEPAGE DESIGN (T.M 1 -)

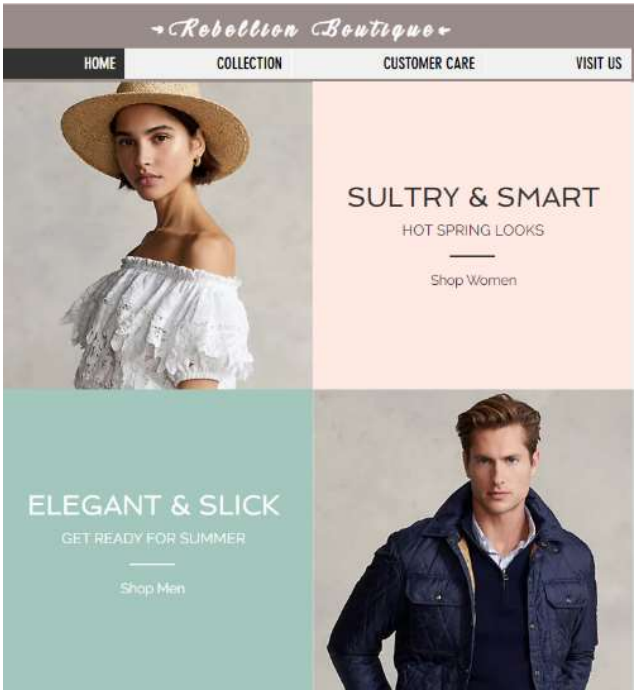

The screenshot on the left side of this report shows the homepage design which includes the company name 'Rebellion Boutique' this has been placed in the middle above the homepage menu. Initially the retail name was located next to the 'Home' button, when this was done it affected the way it looked like the font size was big so to view all the menu options, the website had to be zoomed out to 60% for everything to be clear. For that reason, the title got moved to the middle also, two images have been added to the home page design, this is to attract many customers and demonstrate some of the products that are being sold.

In this screenshot it shows the second part of the homepage design, a 'new arrivals' has been included this is a great feature as it'll constantly be changing as new products will be added – this will ensure customers have an idea of what's new and once it's available they'll have the chance to join the list to receive the latest news on 'New Arrivals' as well as receiving exclusive promotions.

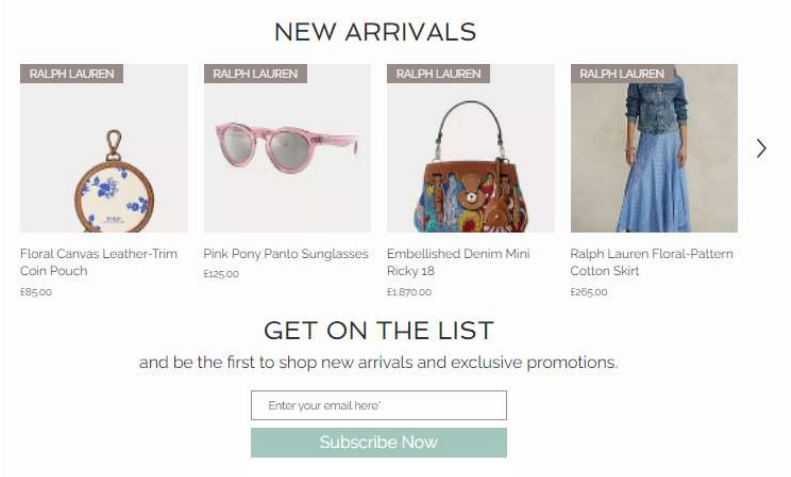

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

MENS AND WOMENS WEAR PAGE (T.M 4 –)

Rebellion boutique has been made with the purpose of attracting both genders (women and men) and so is the design of our website. We segregated both genders within collection and made it a choice of users to select whichever choice of selection.



The most unique part of the men and women home page design is the filter space, it allows less time to waste for the users and easily accessible to shop within price ranges. Which makes it easy to shop within the website.

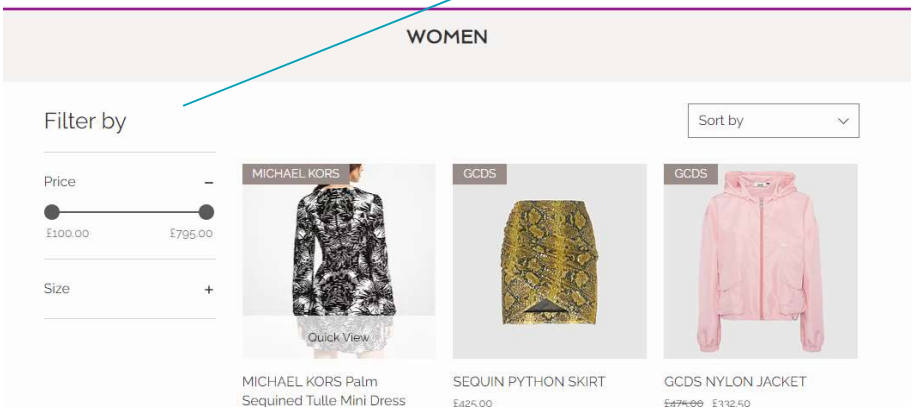

Another beautiful design from this section is the 'sort by' option at the top right-hand corner of the page. It provides different options of sorting, from the newest collection to alphabetically order of characters that enables customers to shop quicker if they know the kind of brand they trying to shop from our website.



ADDING PRODUCT TO SHOPPING CART (T.M 3 -)

As we know for running a website or any application whether web based or native app there must be a client side and server side, and to have the system properly and smoothly running constantly there is a need for constant and timely maintenance.

This could be in forms of regular update rollouts, bug fixing, security measure upgrades against possible malicious attacks etc which could be time consuming as well as needs resources. Wix saves the business both, resources, and time, all the server maintenance is taken care of by the platform itself, and the only maintenance or upgrades left to the user is their website, for instance upgrade of the layout if needed, adding removing products from the website etc. Thus, we opted to use Wix for our website project.

Adding items to the shopping cart is done when the products are browsed, the item that the user wishes to add to the cart must be clicked on which then opens a subpage where size and quantity of the item is chosen and then added to the cart.

For the item to be added to the cart, the items size and the quantity must be provided, an error will be given, and the item will not be added to the cart otherwise.

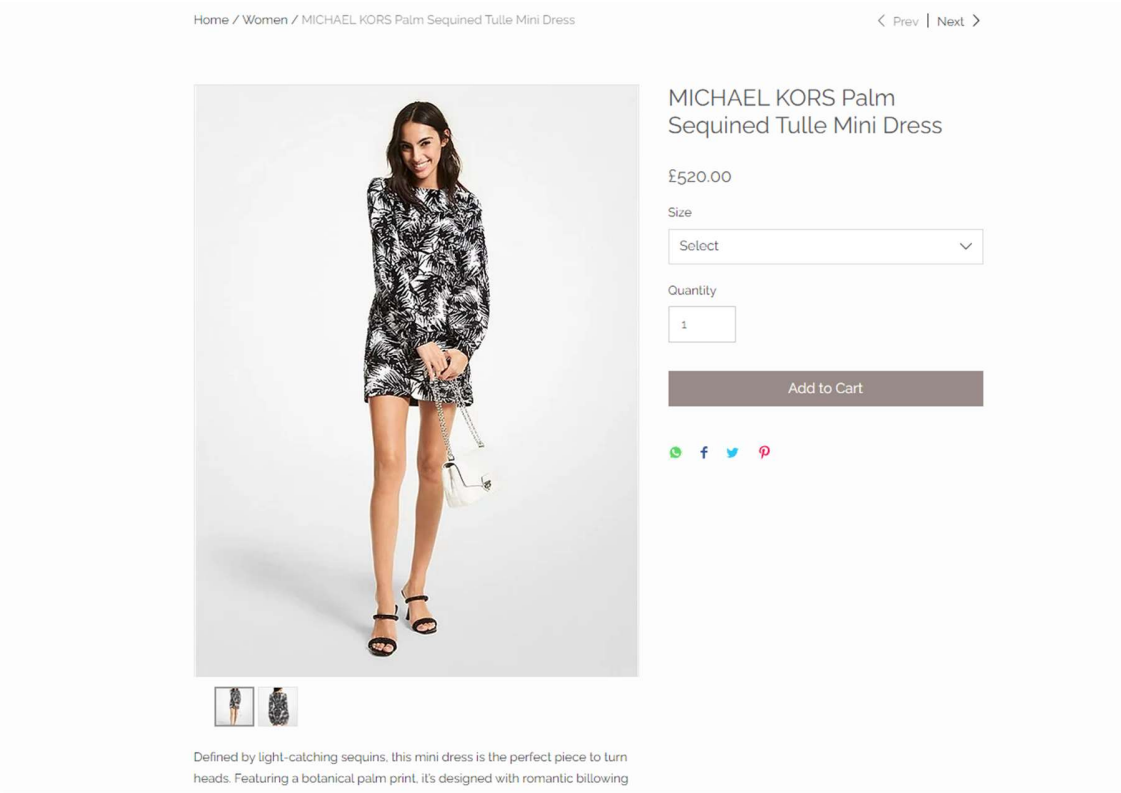

SHOPPING CART (T.M 3 -)

The shopping cart icon is located at the top right corner of the webpage. All the items add to the cart will be stored and will be visible in the cart, the cart can be edited by removing items or increasing and decreasing the quantities.

Upon clicking the view cart button, the cart can be accessed and check out option will be provided to proceed and finish the purchase.

The screenshot below from the main webpage shows the shopping cart button at the top right corner of the screen.



Below is another screenshot which shows the cart from inside and it can be seen there are options provided for the user to remove and decrease or increase the quantity of the items.

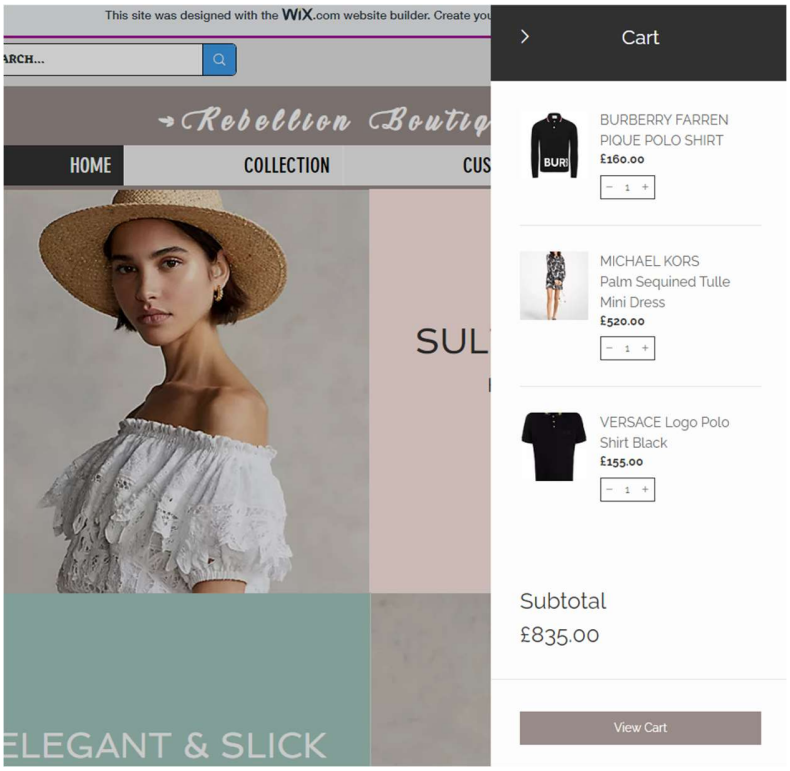

CHECKOUT PAGE (T.M 1 -)

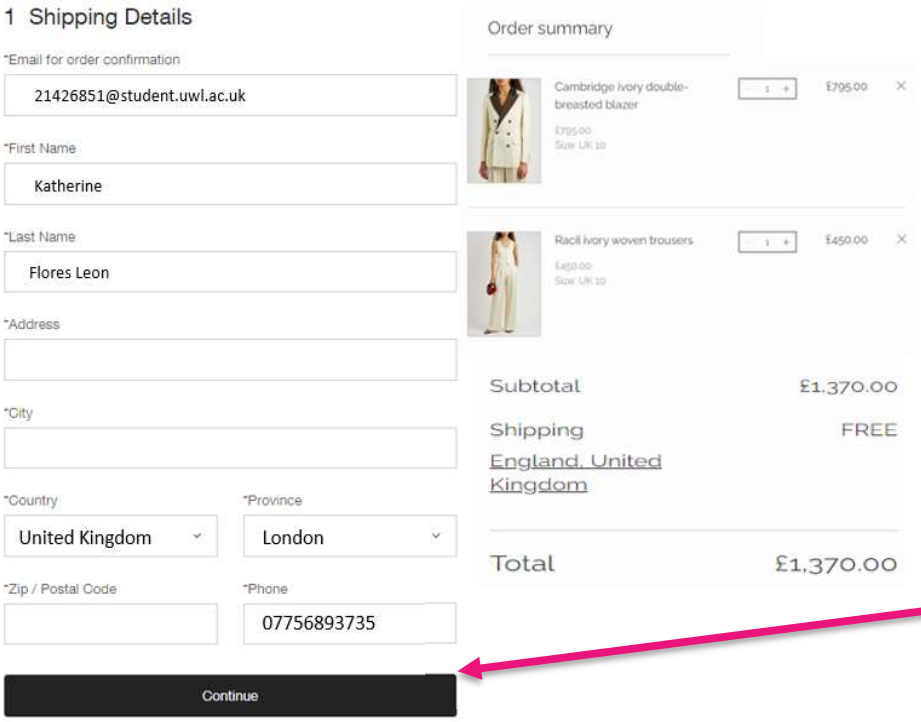

In the left screenshot, I have demonstrated how the checkout page looks like, for example at this stage the user is expected to enter their email address, mobile number, first name along with their address. Once they have entered the required information, they will be able to select "continue" to finish of their order.

Once the customer has selected the "Continue" button they will re-directed to the payment page, a screenshot has been provided on the left side. As shown in the image, the user must enter their card details as they selected to pay with a "Direct Debit" card, besides that the user will continue seeing the products which will be purchased as well as the total amount to pay.

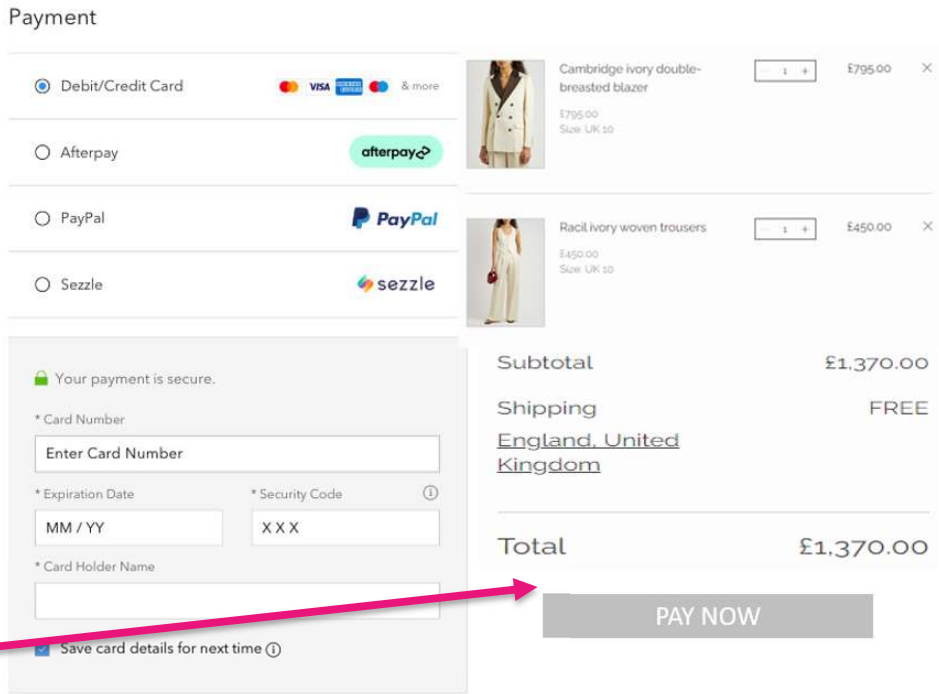

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

USER CREATING ACCOUNT & LOGGING IN (T.M 1 –)

In this section of the report, screenshots have been shown below to demonstrate how a user creates an account or logs into their account which has previously been created.

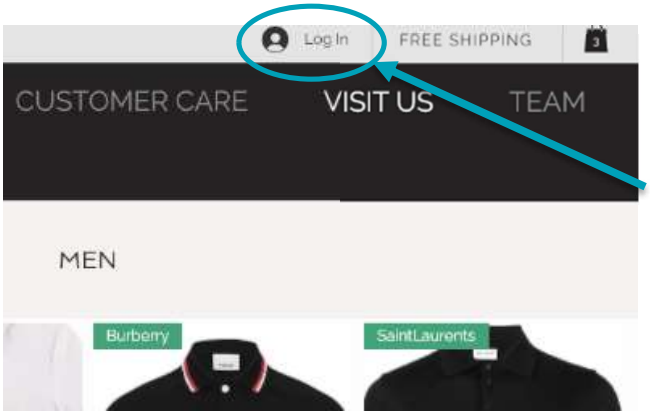

For the customer to directed onto the signing up or logging page they must click the "Log In" button first which is located at the very right-side corner of the website.

Once the customer has clicked the "Log In" button they will be redirected to this page as shown on the right-side screenshot. At this stage the customer will be shown several options if they haven't already created an account. For example, in this screenshot its shows that the client can create an account by signing up with their Facebook or Google account. Many users may find this easier and quickly to do, although others may prefer to go for the third option which is simply Signing Up with their chosen Email Address.

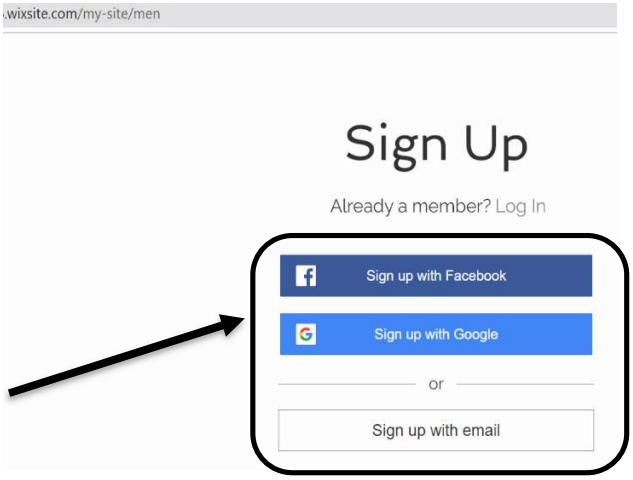

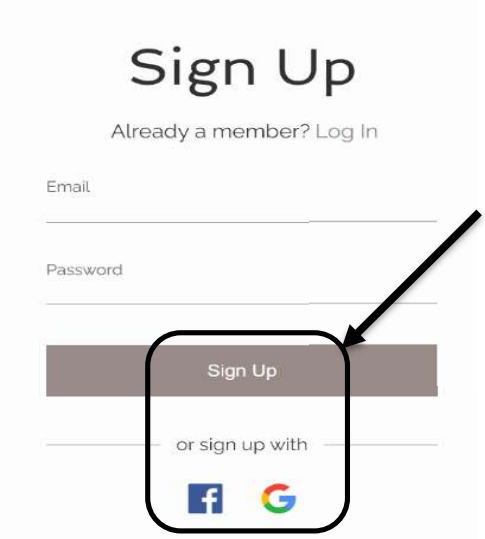

The customer will be able to sign up by putting down their chosen email and password – after this the customer won't need to add any more information and simply select the "Sign Up" button.

Once the registration has been successful, they will be able to add products on their Wishlist, log out to keep their account safe, update their Payment Card, checkout any subscriptions etc.



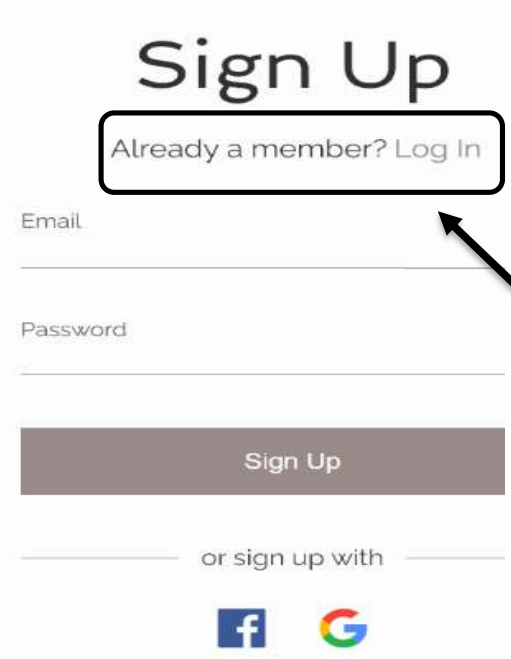

If the customer wants to log in into their account, they'll realise that they have been redirected to the "Sign Up" page, however the customer will be shown the following question "Already a member?" with a "Log In" link next to it. The customer must click on this link so they can be taken to the correct page.

Once they have clicked the "Log In" link the customer will be shown three ways to log into their account either by Facebook , Google, or their personal account info.

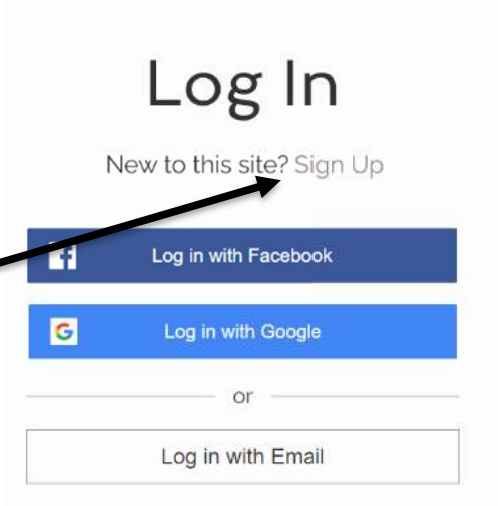

Apart from this, if a user has been directed to this page by accident and instead wanted to create an account they can simply click on the "Sign Up" link which is located underneath the "Log In" title.

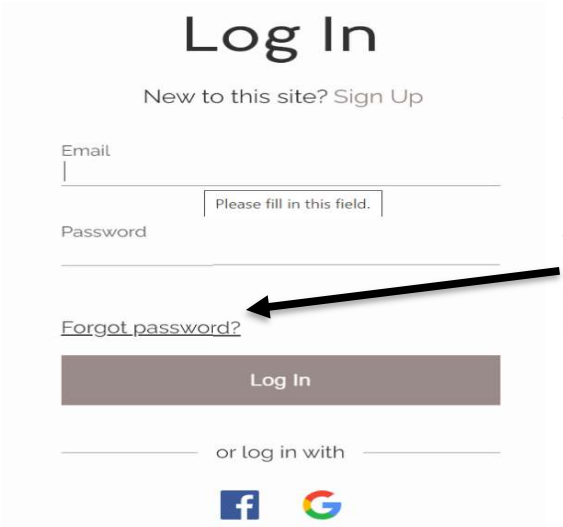

If the customer has chosen to log in with their email, they will be asked to enter their email address and password. If the customer has forgotten their password, they can create a new password by clicking the "Forgot Password" link and simply follow the instructions.

Website Functionalities

QUICK VIEW PRODUCT & SHOPPING BASKET PANEL (T.M 1 –)

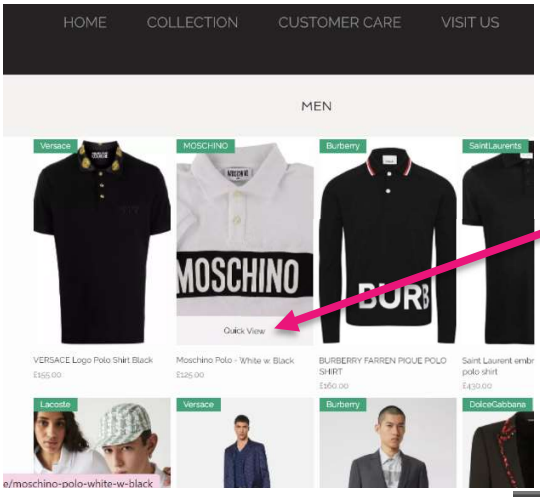

Quick View is a feature which lets customers view any product when browsing without redirecting them to the product page. This can be very beneficial for customers who want to browse through the products quickly and simply want to get a glimpse of the item.

Once the customer has clicked "Quick View" a small tab will appear where it will show the customer the picture of the item, product name and price; besides this they're able to add the item onto their shopping basket once they have selected a size and entered the number of quantities needed.

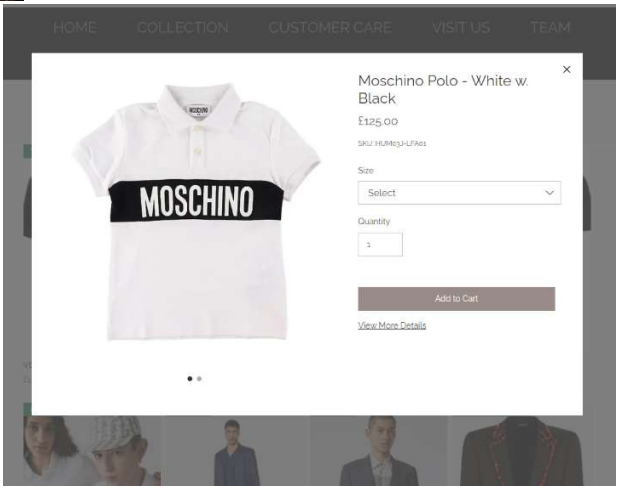

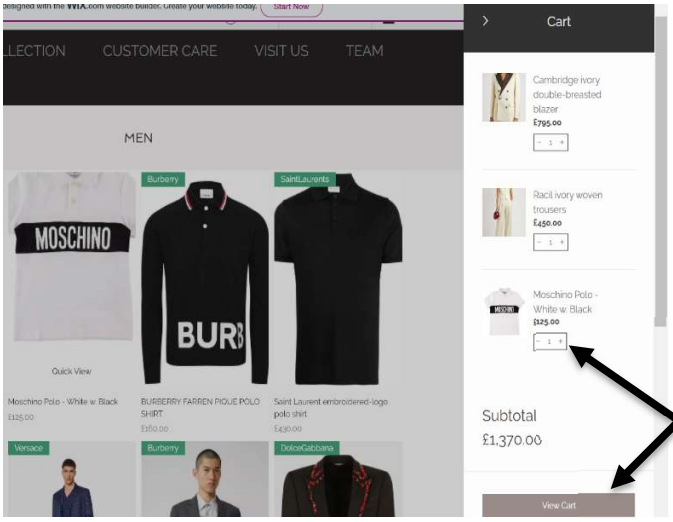

Another website feature is, as a user adds a product to their shopping basket via the "Quick View" feature a Shopping Basket panel will appear on the right side of the website as shown in the screenshot provided. This panel will contain information of all the products which were added to the basket by the user along with giving the customer the option to adjust the quantity. Also, a "View Basket" button will be available once the customer is ready to view their order.

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

FORM TO CONTACT STORE/STAFF (T.M 4 –)

As a company, we want our customers to feel and enjoy their experience with the company either when buying or using the website for any services. And the best way to do this is the provision to contact the company for any queries, complaints, and feedbacks as this would help the company in satisfying most of customers' needs.



Below Rebellion Boutique's website page is a contact us link that enable customers to have a direct communication with the company either through phone calls or a form

Above is also a customer care option that we have provided to help customers navigate through the website with ease I.e., customers can use any of the options (contact us or customer care above to contact the store for anything with the use of the form provided. The form allows us to get back to the customers about any queries made as it requests for the customers' name and email for easy contact. Furthermore, is a message box that allows the customer to express their difficulties or feedback.

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

ONLINE CHAT FACILITY (T.M 4 -)

Online chatting is a tool we have added to our page as it provides customers with different options when in need of a support from our website or services we are providing. Calling and emailing can be really exhausting for some customers as it could be time consuming to get a reply. However, with the use of online chatting, you get to find some answers to most queries immediately as some could be automated from pre scripted questions and answers.

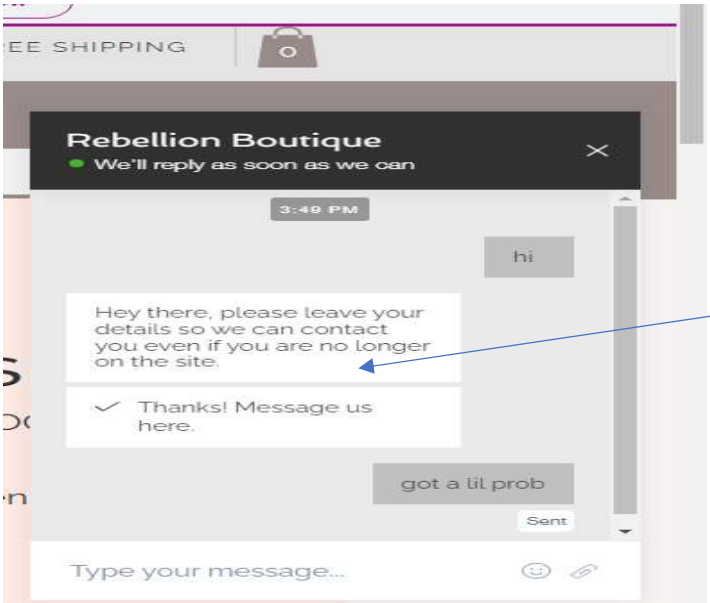

When using the internet for anything, there are chances a lost connection could occur, and as a way of caring and helping our customers, all customers are required to put their details starting from their name and email for a chance to reconnect with them to complete their request from the chat.

SOCIAL FOOTER (T.M 4 -)



Our brand is built to please and satisfy customers by making sure we stay on top of every trend and supply our customers with their needs. However, to do this, been socially present is our top priority as this gives our customers every chance to view any new updates and drops from us through different channels e.g., from the website, store, to our different social networks like Facebook, Instagram, twitter, and Pinterest. The icons provided for the different social medias are so powerful because once clicked, it redirects customers to our pages: which serves as an extra promotion.

PRODUCTS VIEW OF THE HOME PAGE (T.M 4 -)

The homepage of the design means everything as it's the first point of contact of our business online i.e., it's been built to attract customers to stay and navigate through the website with a purpose of buying something. So, we have designed the website base on different views such as aesthetics, accessibility, navigations, and products availability.

Aesthetics

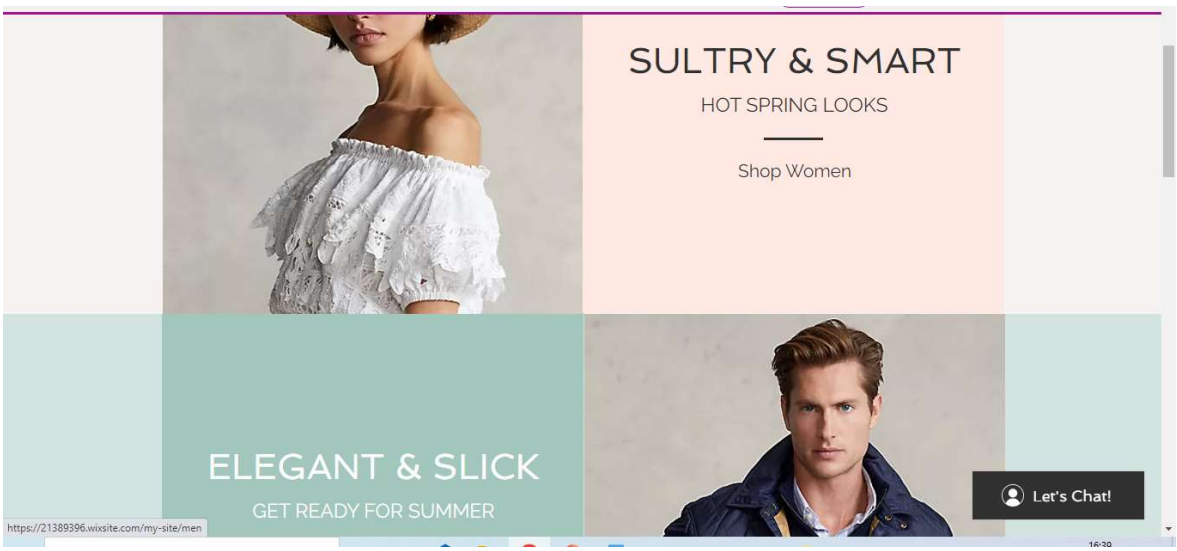

Starting from the colour of the website, you can clearly tell we went for the colour and shapes that both genders would appreciate. So simple, but attractive. A square like picture, using a grey background for both of our models in the background while both edges are diagonally connected. Also, the other sides of the shapes are clearly describing what we sell but with different colours, choosing pink for ladies and while blue is for the men on the item that is been advertised. The sequence and colours are so beautiful to watch, and we can only say well done to our creative minds for this.

Accessibility



We are targeting different kinds of customers i.e., we are inviting all shades of customers with disability to feel welcome to shop on our page e.g., customers with bad sights have been considered whilst creating the website as we made sure all text are big enough for visibility. Also, provision of searches to help them with their shopping.

Navigations



We all want to enjoy the feeling of using something, and this goes also to our website, we have made the website feels like child play when visiting our page. The two arrow bars facing different directions as provided easy viewing of the products on display. This makes shopping easy and could increase chances of customers buying from the list.



Another feel from using the website is the way you can easily navigate from the homepage of the website to selections of items we sell by just going on the collection category. This provides easy room to choose what to shop within seconds of being on the webpage. This service could motivate customers to explore the webpage more.

Products availability/display



Having this kind of features makes customers aware of our new drop and trend, and most likely shift their attention into checking out and end up buying any of our fashion wears from just visiting the webpage.

DISPLAYING PRODUCTS (T.M 5 -)

Products on the website can be displayed by either using the search bar or the collection button. If the user uses the collection button, the user has an option of choosing from the various categories. That is either women, men, accessories, or sales. The page below shows the clothes that display when the customer selects the "women section". The categorization of the product enables customers to find specific items without having to search through all products.

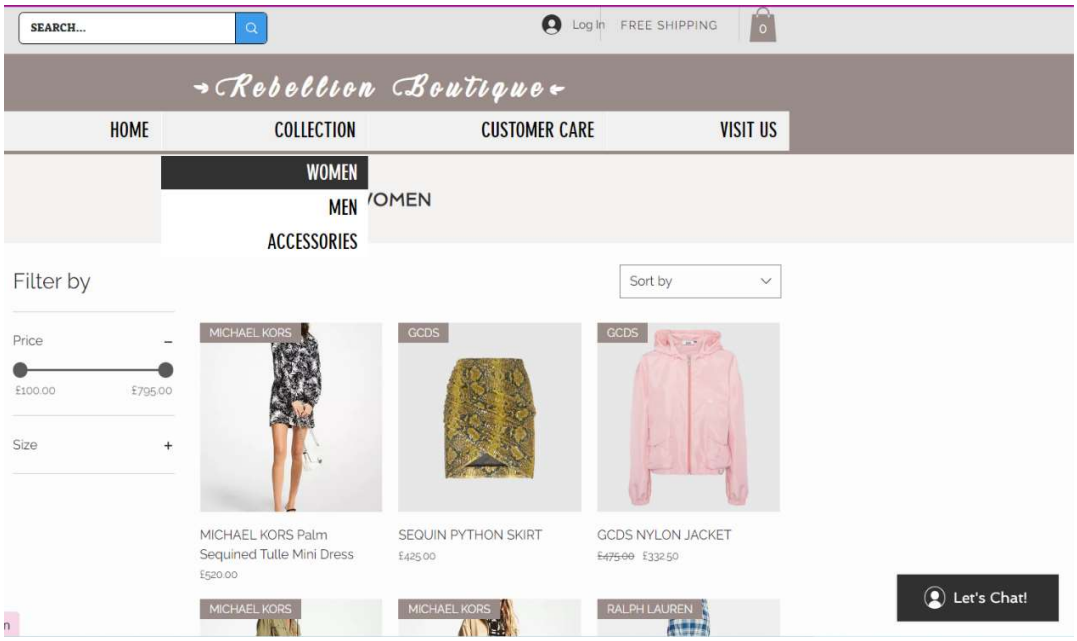

When the customer clicks on a product, the selected product page is opened. The new page allows the customer to view different angles of the product by clicking on the images.

1. **Images that show different angles of the item.**

1

PRODUCTS FILTERING (T.M 5 -)

Product filtering has been added on the product page to give customers option to search for specific items, whilst sorting is included to rank items either by alphabetical order, or newest to oldest. These features will not only reduce thousands of products into manageable amount, but they will also order products in way that meets customer's needs. This may increase the likelihood of users deciding to make a purchase in shortest possible time.

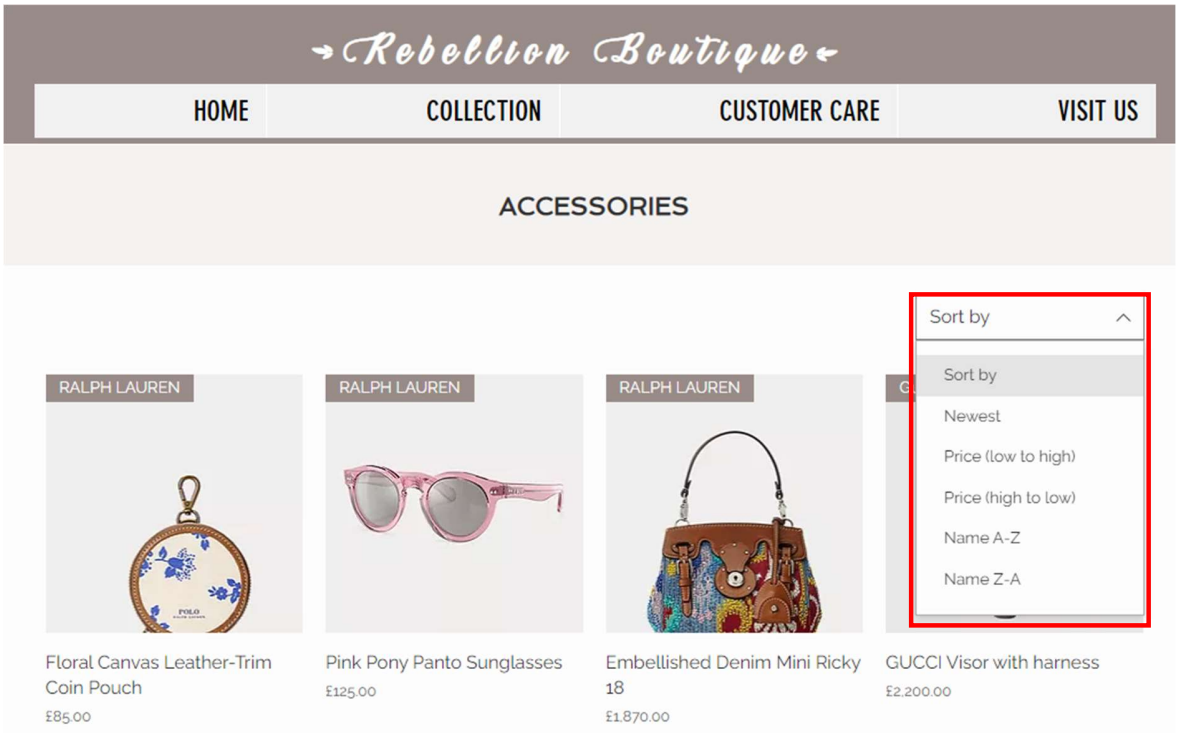

1. **Sort by**
2. **Filter by**

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

PRODUCTS DESCRIPTION (T.M 5 -)

Product description includes both a quick product description and a detailed product information. The quick description basically tells the customer what product it is. For example, La Greca Gabardine Blazer, whilst the detailed product information informs the customer about styling options, fabric details and care.

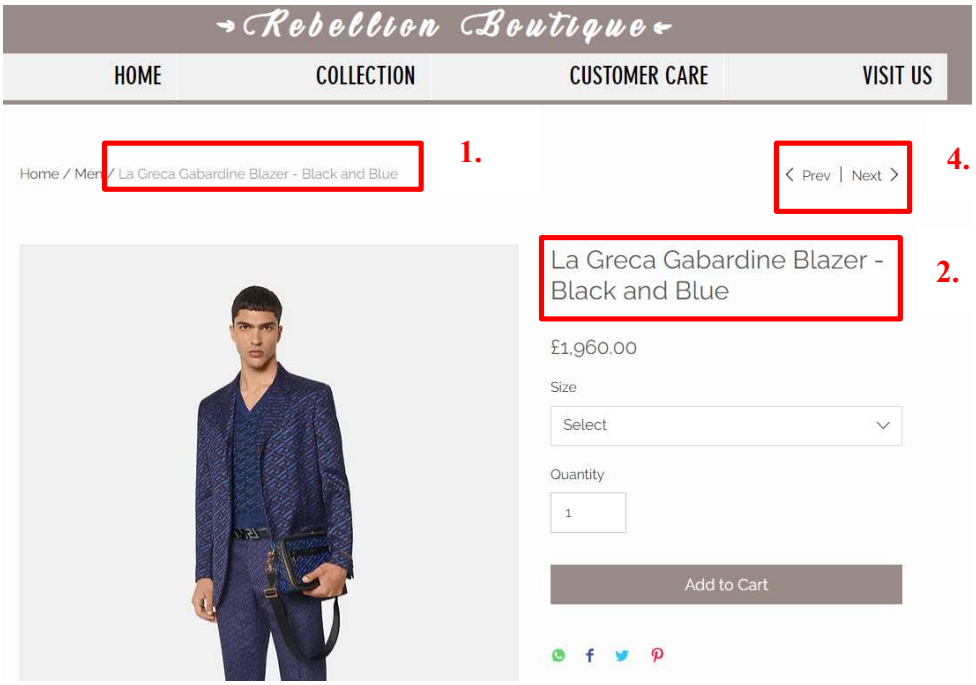

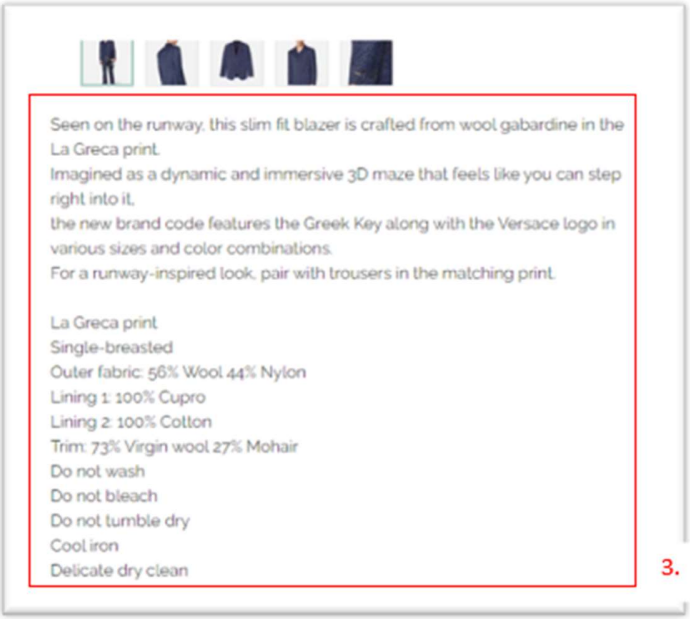

1. **Product page: Men's Section**
2. **Quick product description.**
3. **Product Information**
4. **Buttons that allow the customer to view previous or next product.**

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

ADDING PRODUCTS TO SHOPPING BASKET (T.M 5 -)

Items can only be added to the cart only if the item is in-stock. Adding items can be done at the product page. Before adding items to the cart, the customer needs to select "size" and "quantity". After selecting the size and quantity, the customer can simply put the items into the baskets by clicking "Add to Cart". Once an item has been added to the basket, a pop-up page appears on the side which informs the customer that the product has been added with a subtotal displayed at the base. The quantity can be edited inside the cart. The customer then has option of closing the cart to continue shopping or view inside the cart.

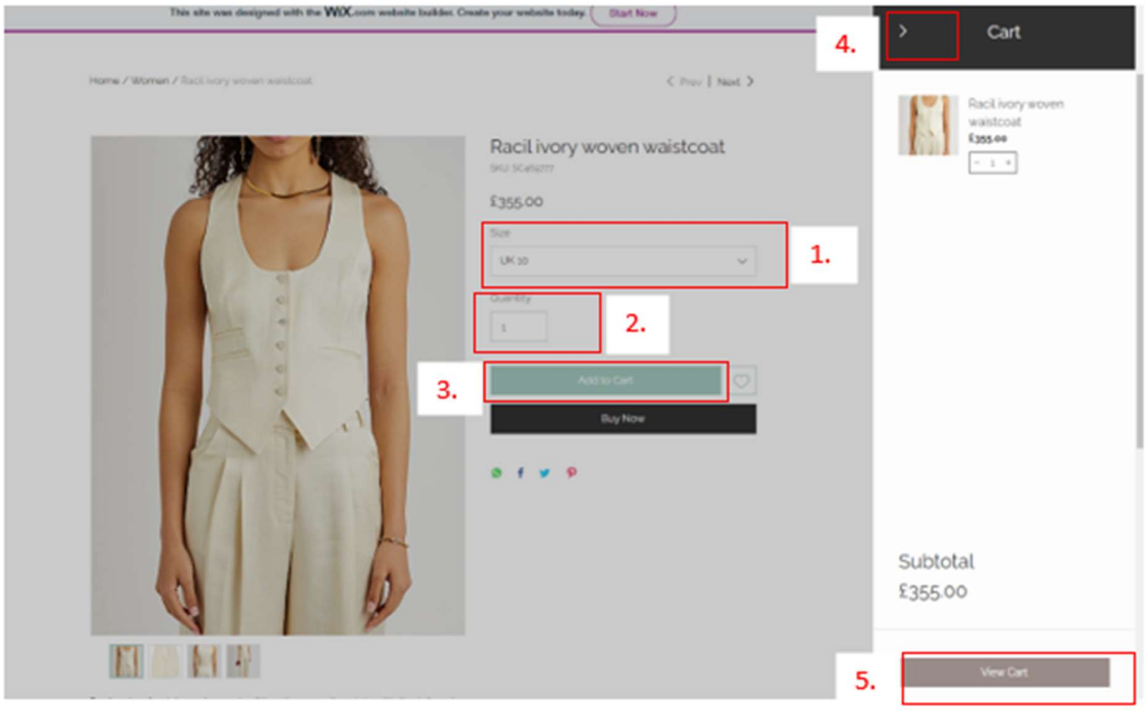

1. Size 2. Quantity 3. Add to Cart 4. Close cart 5. View Cart

EDITING SHOPPING BASKET (T.M 5 -)

The customer can edit the cart at the "My cart" page. This page displays all items that has been added, with their quantities, subtotals, shipping fee and a grand total. On this page, customers can add or reduce to the quantity of an item by using the "+" sign. If the customer wants to remove an item, they can simply click on the "X" sign.

A promo section has been included to allow loyal customers with discounts to enter their discount codes. There is a section to add notes for delivery.

Rebellion Boutique operates only in the United Kingdom and items are on the expensive spectrum, therefore, it was agreed that shipping cost will be free for all customers. For our customers to feel safe on our website, checkout payments are secured.

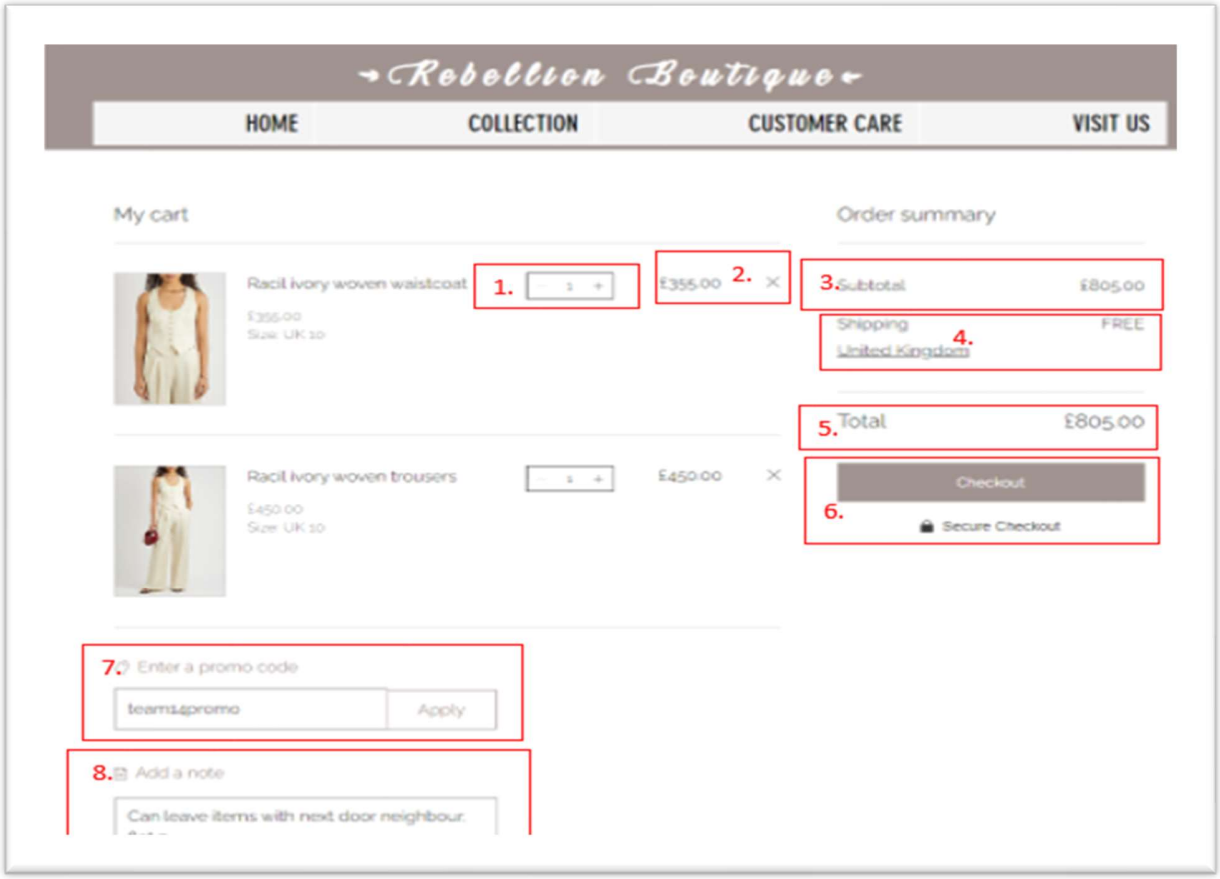

1. **Quantity of items**
2. **Removing of items**
3. **Subtotal of an item**
4. **Add a note**
5. **Shipping (Free)**
6. **Promo Code**
7. **Total**

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

Testing Website

SIGNING UP (T.M 3 –)

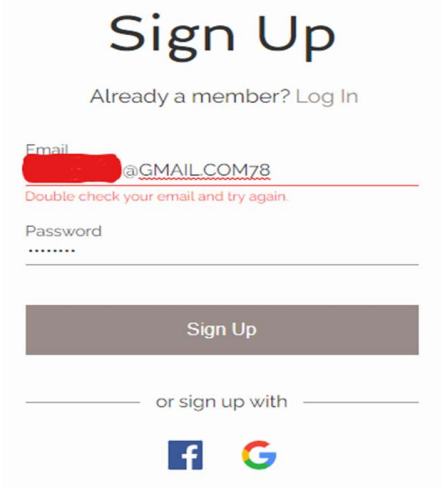

Above is a screenshot of the sign-up page where incorrect email is provided, and an error is given.

Domain	Input	Result	Outcome
Yahoo	**********@yahoo.com45	Error	Fail
Yahoo	********@yahoo.com	Registered	Pass
Google	sign up with google	Registered	Pass
Facebook	sign up with Facebook	Registered	Pass
Gmail	********@gmail.com	Registered	Pass
Gov	*******@gov.co.uk	Registered	Pass
Gmail	TEST@GMAIL.COM	Registered	Pass
Uwl	******@UWL.AC.UK	Registered	Pass
Uwl	*********@UWL.STUDENT.AC.UK	Registered	Pass
Blank	*********@	Error	Fail
Gmail	*********@GMAIL	Error	Fail
Non Existing	*********@.GMAIL.COM	Error	Fail
Gmail	@gmail.com	Error	Fail

* To register on the website, an email address with a proper domain name ending must be provided.

* The registration form is CASE friendly, both small and capital letters are accepted.

* Username only is not accepted.

* Emails already registered on the website are not accepted.

* Emails must have letters before @ the domain name

LOGGING IN (T.M 3 –)

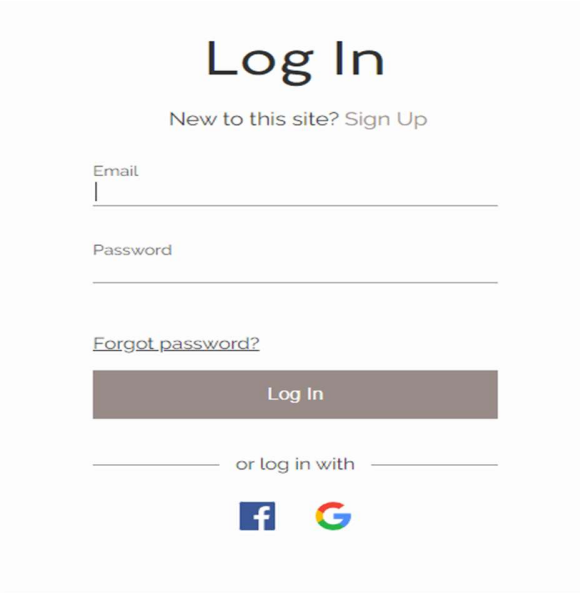

Email	Password	Result
Match	Wrong	Fail
Wrong	Match	Fail
Match	Match	Pass
Wrong	Wrong	Fail
Unregistered	Unregistered	Fail

* Both email and password should match with the registered details on the website to log in to the account.

* If either of the input fields are provided with data that does not match the database the request will be rejected.

* If the user has forgotten the password a reset password link is provided where an email will be sent the registered email to reset the password.

* Any email that is not registered on the website will not be allowed to log in.

BROWSING OF WEBSITE (LINKS) (T.M 3 –)

Action	Output	Result
Click on Home	Redirect to Home page	Pass
Search Bar	Returns search	Pass
Click Collection	Returns categories of products	Pass
Click customer care	Send message to the seller	Pass
Click Visit Us	Provides info and address about the business	Pass
Click Team	Provides info about the team	Pass
Click Cart	shows items added to the cart	Pass
Click Team member	Returns subpage containing the team member information	Pass

* Most of the website options are using clicks to open a subpage.

* Search bar of the website sees user input data to return results for the products user is searching.

CONTACTING PAGE (T.M 3 –)

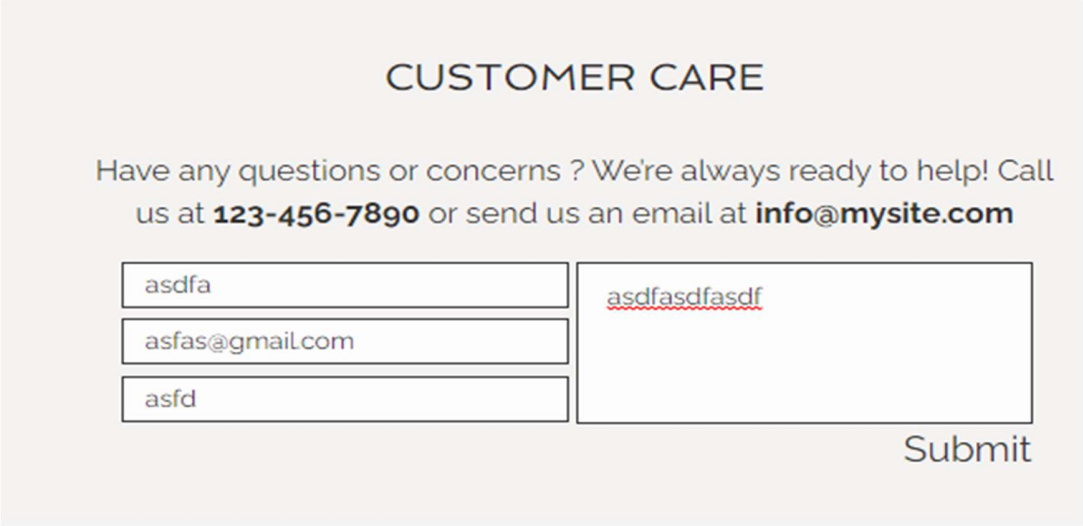

Above pictures shows a customer contacting the seller via the customer care service of the website.

Below is another picture of the message received by the seller.

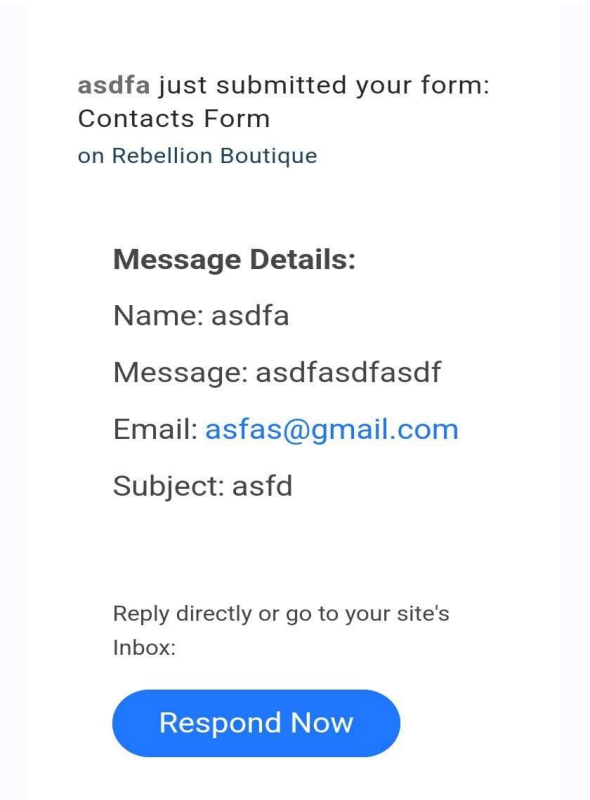

Once the query is received by the administrator, it will be addressed at the earliest opportunity.

Name	Email	Subject	Submit	Message	Result
Blank	Filled	Filled	Yes	Blank	Fail
Filled	Blank	Filled	Yes	Filled	Fail
Filled	Filled	Blank	Yes	Filled	Fail
Filled	address doesn't have domain ending	Filled	Yes	Filled	Fail
Filled	Filled	Filled	Yes	Filled	Pass
Filled	Filled	Filled	Yes	Filled	Fail
Filled	Filled	Filled	No	Filled	Fail

* All the input fields require inform and must be filled otherwise given error.

* Emails must have a proper domain name ending.

* After filling the input fields the Submit button must be clicked or message won't be sent to the seller.

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

COMPLETING PAYMENT (T.M 3 –)









Email	FirstName	LastName	Address	City	Country	Province	PostCode	Phone	Payment Mthod	Card/ID Details	Pay Now	Purchase
Empty	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Clicked	Failed
Filled	Empty	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Clicked	Failed
Filled	Filled	Empty	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Clicked	Failed
Filled	Filled	Filled	Empty	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Clicked	Failed
Filled	Filled	Filled	Filled	Empty	Filled	Filled	Filled	Filled	Filled	Filled	Clicked	Failed
Filled	Filled	Filled	Filled	Filled	Empty	Filled	Filled	Filled	Filled	Filled	Clicked	Failed
Filled	Filled	Filled	Filled	Filled	Filled	Empty	Filled	Filled	Filled	Filled	Clicked	Failed
Filled	Filled	Filled	Filled	Filled	Filled	Filled	Empty	Filled	Filled	Filled	Clicked	Failed
Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Empty	Filled	Filled	Clicked	Failed
Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Empty	Filled	Clicked	Failed
Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Empty	Clicked	Failed
Wrong domain	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Clicked	Failed
Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Clicked	Pass
Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Not Clicked	Failed
Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Filled	Inaccurate	Clicked	Failed

* All the input box fields must be filled for the payment to be processed and successful purchase.

* Incorrect Card Num/ ID will result in unsuccessful purchase.

* Pay Now button must be clicked once all the details are provided, no payment will be processed otherwise.

* Wrong email address such as missing domain name, missing @, missing . Will result in error.

* Only one payment method must be selected.

Group Activities

WORKLOAD (T.M 1 –)

<Image removed to protect anonymity>

Above, a screenshot of workload has been attached – having a workload is very significant as it's much easier to stay organised as a team, apart from this, it clearly demonstrates the tasks that each person has been given which includes due dates and the priority of each task – it's very useful as the team leader or team manager will be able to look at the task status of each member whether it has completed or if they need support.

<Image removed to protect anonymity>

This Screenshot show the current tasks which have been assigned to team members it also shows whether they have completed their tasks in time.

<Image removed>

In this screenshot, you can see that both team members have nearly completed all the assigned tasks – it also gives the impression that they are still in time to complete their

tasks. The tasks which have been assigned to each user shows the level of priority of each task this is meant to give the customer an idea of how important their tasks are.

DELIVERABLES (T.M 1 –)

- Presentation completed : 18th of March
- Testing website functionality : 12th May
- Demonstration of website : 20th of May
- Add products on website : 15th of April
- Time for Adjustments and changes : 20th of April
- Testing website functionality : 15th of May
- Implementation time for fixes and bugs to be found and resolved

Project completion : 20th of May

<Image removed>

GROUP MEETINGS (T.M 1 –)

<Images removed>

The screenshots on the right side of this report, demonstrate how we created a journal entry of the meetings we had as a team, for example, we got together to discuss our group work on 25th April we also met on the 22nd of March.

GROUP COLLABORATIONS (T.M 1 –)

<Image removed>

The screenshot on the right-side shows, how we collaborated as a team – as shown most of the team members uploaded their piece of work that they were assigned with, this log includes the date and time each member uploaded their work, it also includes their full names.

<Image removed>

On the right side, there's two screenshots which show team members have emailed each other their completed work in a Word File, this is useful as if improvements need to be done then it can easily be updated.

Module Leader: Dr Maria Winnett
Module: Group Project Report
Group Name: The Five

GROUP MEETING MINUTES (T.M 1 –)

Date: 12/05/2022

Time: 09:00

Facilitator: xxxxxxx

Team:

| xxxxxxx

Time	Topic	Present
45min	Welcome	All members
60min	Assigning Tasks	Present Members: 1,3,4 & 5
120min	Designing Website in Sketches	Member: 1
450min	Developing Website	Members: 1 & 2
80min	Face-2-Face Meeting – Catching Up	All members
90min	Gantt Chart, Project Plan, PERT Chart	Members: 4
120min	Testing Website	Members: 3
200min	Project Risk Register Personal Risk Register Sequence Diagram	Members: 1
230min	Project Team Roles/Requirements Project Team Charter Literature Review	Members: 5
360min	Project Documentation Project Functionalities	Members: All members
120min	Group Activities	Members: 2
60min	Final Group Meeting	Members:

		All members

Challenges (T.M 1 –)

Throughout the development of the website and writing the report as a team we faced several challenges such as withholding information, reduced engagement along with allocation of work tasks, development of website.

While developing the website, we thought that developing the website using WIX would be the best option as we didn't have a great amount of knowledge based on front-end and back-end of a website. With WIX we managed to add all the essential features and added various products as our aim was to include more than 20 products for the website – to complete the website we had to design the way it would look like and how things would be located.

At the beginning of planning the report, we had a meeting to allocate tasks between each other however, the second team member wasn't present, and we had no option but to go ahead with the 'tasks allocation' we then shared the tasks which included each team members name in a group chat that was created by another team member. Having created this group chat ensured that we were able to communicate and share any struggles that we had, we all tried to engage and set up meetings every Tuesday as this would be the day all four members were coming to university; again we had one team member that didn't turn up every Tuesdays – we tried to ensure that this absence didn't impact the team negatively, as everyone was given their tasks and most members knew what to do it showed a sign that they didn't struggle and had a good idea of what to do.

Besides that, when we reached the section of testing and documentation of the website, several team members and team leader realised that the team member who was administering the website hadn't completed the website as it was only the template was set up and a few products were added.

Due the lack of this, the team leader had made several adjustments to improve the website for example, as mentioned in the report the view of the homepage was way too large and had to be zoomed out to 60% in order for all the features to be seen clearly due to this, the company name had to be moved position, in womenswear section only one product displayed so the team leader added more related products to make a total of 16 products, information and questions section was also missing, visit us section had to be adjusted as well as it showed an address from a different country, filtering and sort by were also missing and much more. As the other three members had very little knowledge in using

WIX and were focusing on other sections such as diagrams, testing etc. the team leader had to make quickly adjust and ensure it met all the user requirements.

Lastly, a great challenged that affected us four was constantly trying to communicate with the 2nd team member this was very difficult as they were never present for meetings never confirmed that they're aware of what to do even though images were provided.

We began to feel very stressed as we all finished our designated tasks, yet the fifth member hadn't communicated with anyone, constantly ignored messages of the team leader, pretty much expected others to complete his work, the only thing this 2nd member was great at was not attending meetings, giving excuses after excuses and lack of engagement.

We've noticed that the fifth member is very uncapable of doing anything on their own and had no interest in the project when we got informed three days before the original due date 20th May that the fifth member was not going to do none of the 7 assigned tasks this meant we had to split it between the four team members, besides that, we already had two other points that needed to get completed.

Many team members felt a lot of pressure and stress due to this shocking news as we all felt that we kept engaged and completed our assigned tasks but now it meant we had to do extra work because the 2nd member was apathetic in the entire duration of the group presentation/report.

References (T.M 1, 3, 4 & 5)

Bell, D. (2004) IBM Developer. Developer.ibm.com. [Online]. Available at: https://developer.ibm.com/articles/the-sequence-diagram/ [Accessed: 1 May 2022]

Byrd, T. and Luthy, R.(2010) 'Improving Group Dynamics: Creating A Team Charter', Academy of Educational Leadership Journal, vol. 14, no. 1, pp. 13-26.

Dilts, B. and Sun, K., 2008. Intelligent Diagramming | Lucidchart. [online] Lucidchart. Available at: <https://www.lucidchart.com/pages/> [Accessed 12 May 2022].

Keith, L. and Gordon, J. (2005) Project management and project network techniques. 7 edn. Pearson Prentice Hall.

Lee, E. (2022) How to take Meeting Minutes. CPD Online College. [Online]. Available at: https://cpdonline.co.uk/knowledge-base/business/meeting-minutes/ [Accessed: 15 May 2022]

Meier, K. (2020) How to Create an Effective Workload Management Process in 2021. Float.com. [Online]. Available at: https://www.float.com/resources/guide-to-workload-management/ [Accessed: 5 May 2022]

NIELSEN, J. - Site Map Usability (Nielsen, 2022) Nielsen, J., 2022. Site Map Usability. [online] https://www.nngroup.com. Available at: <https://www.nngroup.com/articles/site-map-usability/> [Accessed 8 May 2022]

Project Management Institute. (no date) What is Project Management. Available at: What is Project Management | PMI

Ray, S. (2021) What Is a Risk Register & How to Create One. Project Manager. [Online]. Available at: https://www.projectmanager.com/blog/guide-using-risk-register [Accessed: 10 May 2022]

Seymour, T. & Hussein, S. 2014, "The History Of Project Management", International Journal of Management & Information Systems (Online), vol. 18, no. 4, pp. 233.

Seymour (no date) History of Project Management Software: How it Developed. Available at: History Of Project Management Software: How It Developed - Financesonline.com (Accessed: 12 May 2022).

Stobierski, T. (2021) Agile vs. Scrum: What's the Difference?. Available at: https://www.northeastern.edu/graduate/blog/agile-vs-scrum/ (Accessed: 13 May 2022).

Simmons, M. (2021) How to Create a Team Charter (Example Included). Available at: https://www.projectmanager.com/blog/how-to-create-a-team-charter (Accessed: 11 May 2022).

SCHWABER, K. - Agile project management with Scrum (Schwaber, 2014) Schwaber, K., 2014. Agile project management with Scrum. Redmond, Wash.: Microsoft Press.

WINNETT, M. - Introduction to project management and Agile (Winnett, 2022) Winnett, M., 2022. Introduction to project management and Agile. [PDF] UWL Blackboard.

Zinman, E. and Man, R., 2016. Welcome to monday.com | a new way of working. [online] Rebellion-boutique.monday.com. Available at: <https://rebellion-boutique.monday.com/> [Accessed 13 May 2022].
